

ALUMNEX CONNECT

JIRA-BASED AGILE PROJECT EXECUTION AND MANAGEMENT REPORT

Ready-to-Submit Project Documentation

Project	Alumnex Connect - Integrated Alumni-Student Mentorship and Career Ecosystem
Jira Project	Alumnex Connect (KAN)
Jira Board	KAN board
Agile Approach	Agile product management with Scrum governance and flow-based Jira workflow
Documentation Date	06 October 2026
Prepared For	Academic project review / viva / project documentation

Academic evidence note: This report documents the Jira project-management record and current workspace state. It does not claim that the current Jira workspace contains historical Scrum Sprint execution. The connected KAN board is a simple/team-managed board without native Jira Scrum Sprint history.

**Department of Computer Science and Engineering
Kongu Engineering College (Autonomous)**

Document Control

Item	Record
Document title	Alumnex Connect - Jira-Based Agile Project Execution and Management Report
Project identifier	KAN
Primary management tool	Jira Software / Alumnex Connect
Documentation repository	Confluence - My first space
Reporting basis	Connected Jira/Confluence workspace and uploaded Jira/Confluence evidence exports
Evidence date	06 October 2026
Status	Prepared for academic submission

Table of Contents

- 1. Executive Summary
- 2. Introduction and Project Context
- 3. Agile Methodology Adopted
- 4. Requirements-to-Jira Transformation
- 5. Jira Project Configuration
- 6. Product Backlog Structure
- 7. User Stories and Acceptance Criteria
- 8. Estimation and Story Points
- 9. Board Workflow and Work-State Management
- 10. Implementation Subtasks and Traceability
- 11. Release and Phase Management
- 12. Dependency Management
- 13. Defect Management
- 14. Scrum Governance and Ceremonies
- 15. Definition of Ready and Definition of Done
- 16. Jira Reporting, Metrics and Evidence
- 17. Confluence Documentation and Knowledge Management
- 18. How Agile Methodologies Apply to Alumnex Connect
- 19. Project Execution Record
- 20. Challenges, Constraints and Academic Reporting Rules
- 21. Results and Outcomes
- 22. Conclusion
- Appendix A - Epic Register
- Appendix B - Story Register
- Appendix C - Subtask Register
- Appendix D - Bug Register
- Appendix E - Screenshot Evidence Log
- References

1. Executive Summary

Alumnex Connect is an integrated alumni-student ecosystem containing authentication, mentorship, developer intelligence (DevPulse), career and jobs, AI career support, real-time communication, community, mobile access, and security/reliability capabilities. The Jira workspace was organized so that these capabilities can be managed as a coherent Agile product rather than as an unstructured list of features.

The verified Jira project contains 10 Epics, 53 Stories, 20 Subtasks and 5 Bugs, giving 88 Jira issues in total. Five Jira Versions divide the backlog into delivery phases. The workflow uses Idea, To Do, In Progress, In Review and Done. The uploaded Jira evidence and current connected Jira state show that the board has been populated across multiple work states rather than leaving all work in the initial backlog state.

The practical Scrum reference supplied for this report describes a flow from requirements gathering to backlog creation, Epic and Story decomposition, estimation, Sprint Planning, task/subtask execution, Daily Scrum, testing, bug fixing, Sprint Review, feedback, Retrospective and reporting. Those concepts have been mapped to Alumnex Connect, while the Jira configuration limits are explicitly separated from the Scrum process model.

Key project-management result: The report establishes a traceable management chain: product capability -> Epic -> user Story -> acceptance criteria -> implementation Subtask -> workflow state -> release phase -> dependency/defect evidence -> documentation and metrics.

2. Introduction and Project Context

2.1 Project context

Alumnex Connect is designed as an integrated digital ecosystem connecting students and alumni through mentorship, career opportunities, developer activity tracking, AI-assisted career guidance, communication, community participation and mobile access. The Jira backlog groups the product around these functional areas and adds a dedicated governance layer for Agile project management.

2.2 Project management objective

The objective of using Jira is to make work visible, decomposable, traceable and reviewable. Jira acts as the operational record for backlog items, status, defects, dependencies and release grouping; Confluence holds the narrative rules, ceremony guidance, quality gates and project knowledge.

2.3 Why Agile fits the project

The product contains multiple interacting capabilities, external integrations, mobile behavior, AI services and reliability concerns. An incremental Agile model is therefore useful because functionality can be broken into small deliverables, risks can be surfaced as visible work, feedback can be incorporated, and releases can be organized in phases.

3. Agile Methodology Adopted

The project is best described as an Agile implementation with four complementary lenses: Scrum for governance and iterative planning, Kanban for visible work flow, XP for engineering quality practices, and Lean for reducing waste and improving flow.

Methodology	How it contributes	Application in Alumnex Connect
Scrum	Product Backlog, Stories, estimates, Sprint Planning, Daily Scrum, Review, Retrospective, DoR and DoD.	Documented in KAN-55 to KAN-63 and the Confluence playbook; native Jira Sprints are not available on the current board.
Kanban	Visible workflow, WIP awareness, bottlenecks, cycle time and continuous flow.	Implemented directly through the KAN board workflow: Idea -> To Do -> In Progress -> In Review -> Done.
XP	Automated testing, CI/CD, continuous integration, small increments and engineering quality.	Represented by KAN-52 Automated Testing, KAN-53 CI/CD Pipeline and KAN-50 Security Hardening; specific historical XP practices require independent evidence.
Lean	Reduce waste, limit unnecessary handoffs, expose blockers, optimise value delivery and use feedback for improvement.	Supported by visible workflow, dependency links, release phases and the continuous-improvement governance item KAN-63.

3.1 Reference Scrum process used for mapping

The supplied Practical Scrum Process Using Jira document explains a complete example beginning with customer requirements, conversion into User Stories, Epic grouping, priority and Story Point estimation, Sprint creation, task/subtask decomposition, assignment, development, Daily Scrum, testing, bug lifecycle, Story completion, Sprint Review, customer feedback, Retrospective, Sprint completion and reporting. The same lifecycle is used in this report as the reference framework for explaining where each Alumnex Jira artifact fits.

4. Requirements-to-Jira Transformation

The first Agile transformation is from broad product requirements into manageable backlog items. Instead of maintaining all functionality as large feature statements, the project converts capabilities into Epics and then into user-value Stories.

Agile step	Alumnex Connect application
Requirement capture	Identify the user or business outcome to be delivered.
Epic grouping	Group related functionality into a coherent product capability.
User Story creation	Express a feature using the user/goal/benefit pattern.
Acceptance criteria	Define observable conditions that determine whether the Story is complete.
Estimation	Record a relative effort/complexity estimate.
Implementation decomposition	Create Subtasks for the technical work needed to satisfy the Story.
Workflow execution	Move work through the board as it is refined, developed and reviewed.
Quality and feedback	Track Bugs and review evidence before marking work complete.
Release grouping	Assign work to the appropriate delivery phase.

4.1 Evidence: Jira backlog

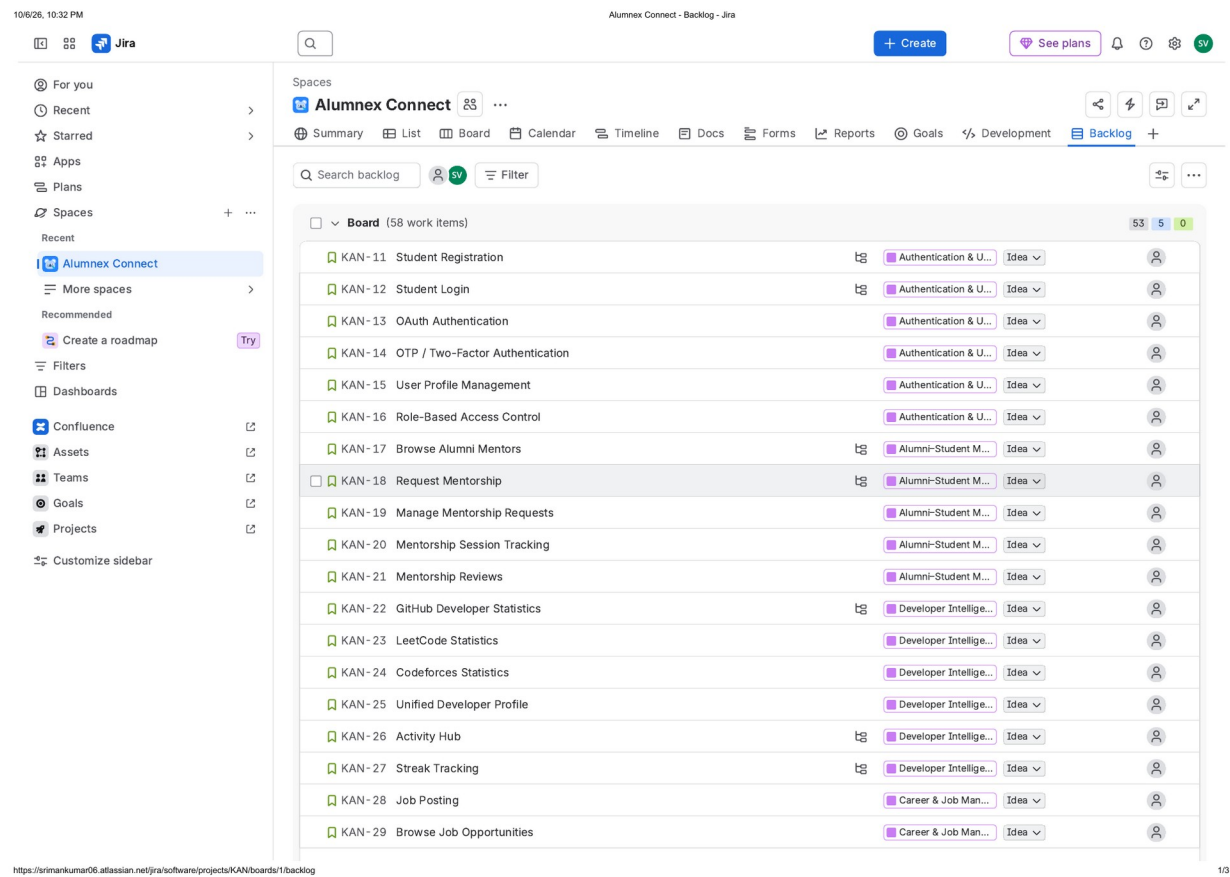


Figure 1. Jira Backlog view showing the Alumnex Connect backlog and grouped Epic/Story structure.

KAN - 30	Apply for Jobs	Career & Job Man...	Idea	▼	
KAN - 31	Job Application Management	Career & Job Man...	Idea	▼	
KAN - 32	ATS Resume Analysis	Career & Job Man...	Idea	▼	
KAN - 33	AI Career Mentor	AI Career Assistant	Idea	▼	
KAN - 34	Skill Gap Analysis	AI Career Assistant	Idea	▼	
KAN - 35	AI Mock Interview	AI Career Assistant	Idea	▼	
KAN - 36	AI Provider Failover	AI Career Assistant	Idea	▼	
KAN - 37	Real-Time Chat	Real-Time Commu...	Idea	▼	
KAN - 38	Chat Groups	Real-Time Commu...	Idea	▼	
KAN - 39	Online Presence	Real-Time Commu...	Idea	▼	
KAN - 40	Read Receipts	Real-Time Commu...	Idea	▼	
KAN - 41	Real-Time Notifications	Real-Time Commu...	Idea	▼	

Figure 2. Continued Jira Backlog view showing additional Alumnex Connect Stories.

5. Jira Project Configuration

The connected workspace identifies the project as Alumnex Connect (KAN) with a built-in board named KAN board. The board is a simple/team-managed configuration. The verified board columns are Idea, To Do, In Progress, In Review and Done.

Configuration item	Verified value
Project key	KAN
Project type	Team-managed / simple
Board	KAN board
Workflow	Idea -> To Do -> In Progress -> In Review -> Done
Issue types in the project	Epic, Story, Subtask, Bug
Jira Versions	5 delivery phases
Recorded dependency links	8 Blocks links
Confluence space	My first space (MFS)

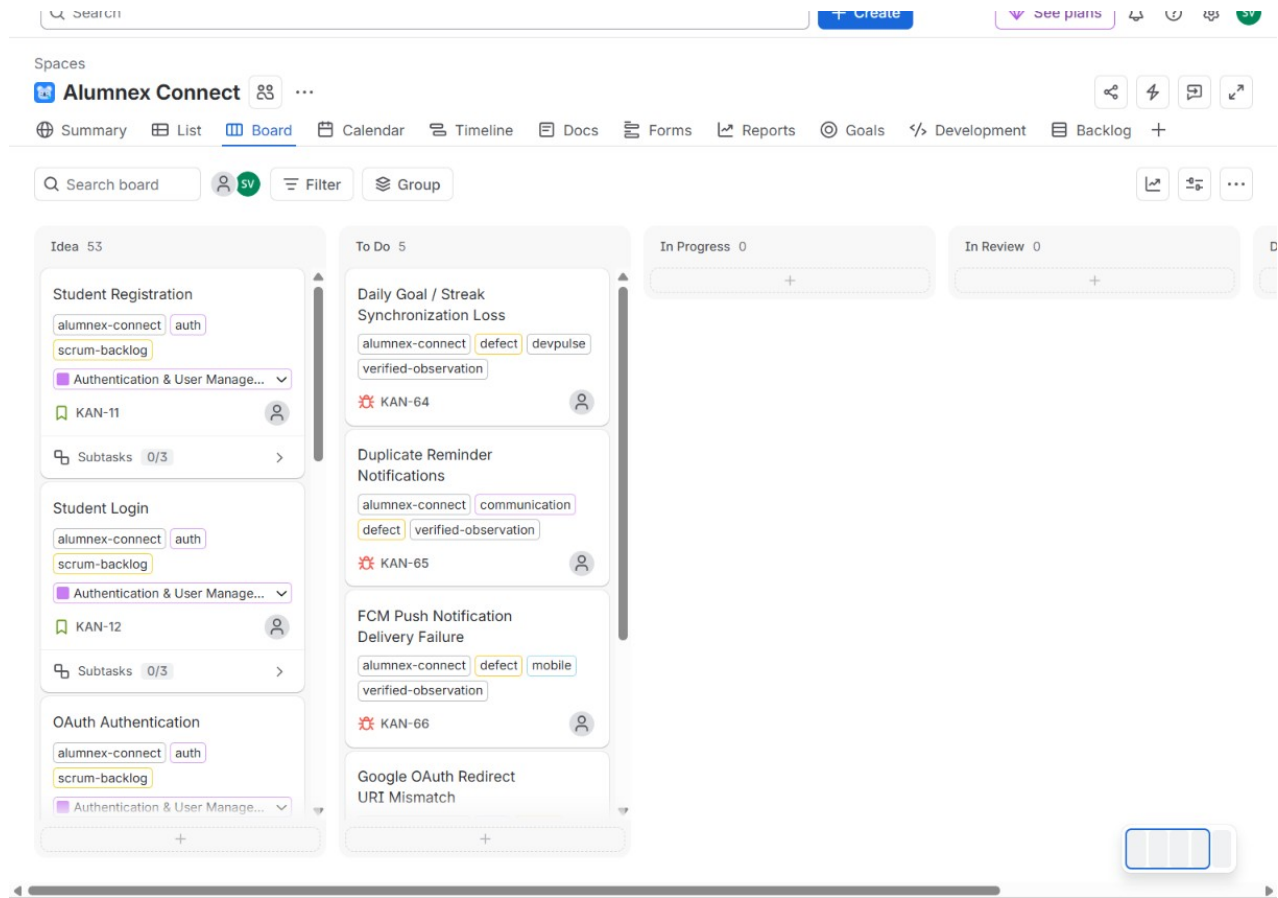


Figure 3. User-provided Jira Board screenshot before workflow population: 53 board Stories were in Idea and 5 Bugs were in To Do.

6. Product Backlog Structure

The backlog is organized into four principal issue layers. Epics provide the strategic capability boundary. Stories represent user-value increments. Subtasks represent implementation activities. Bugs represent quality deviations that require corrective work.

Issue type	Purpose	Agile role
Epic	Large capability or outcome	Roadmap and product structure
Story	User-visible outcome	Product Backlog and incremental delivery
Subtask	Concrete implementation activity	Development execution and traceability
Bug	Observed defect/deviation	Quality management and release readiness

6.1 Epic register

Key	Epic	Purpose
KAN-1	Authentication & User Management	Identity, registration, login, OAuth, OTP, profiles, RBAC
KAN-2	Alumni-Student Mentorship	Mentor discovery, requests, sessions, reviews
KAN-3	Developer Intelligence - DevPulse	Coding-platform integrations, activity hub and streaks
KAN-4	Career & Job Management	Job posting, browsing, applications and

		ATS
KAN-5	AI Career Assistant	AI mentor, skill-gap analysis, mock interview and failover
KAN-6	Real-Time Communication	Chat, groups, presence, read receipts and notifications
KAN-7	Community & Events	Forum, events and alumni networking
KAN-8	Mobile Application	Android wrapper, mobile authentication, responsive UI and push
KAN-9	Security, Reliability & DevOps	Security hardening, failover, testing, CI/CD, monitoring
KAN-10	Scrum & Project Governance	Backlog, ceremonies, quality gates, risks, releases and metrics

7. User Stories and Acceptance Criteria

The Stories follow the user-story structure described in the supplied Scrum reference: As a <user>, I want to <perform an action>, so that <benefit>. In Alumnex Connect, the descriptions also include explicit Acceptance Criteria and a Suggested estimate. This combination supports backlog refinement, implementation and review.

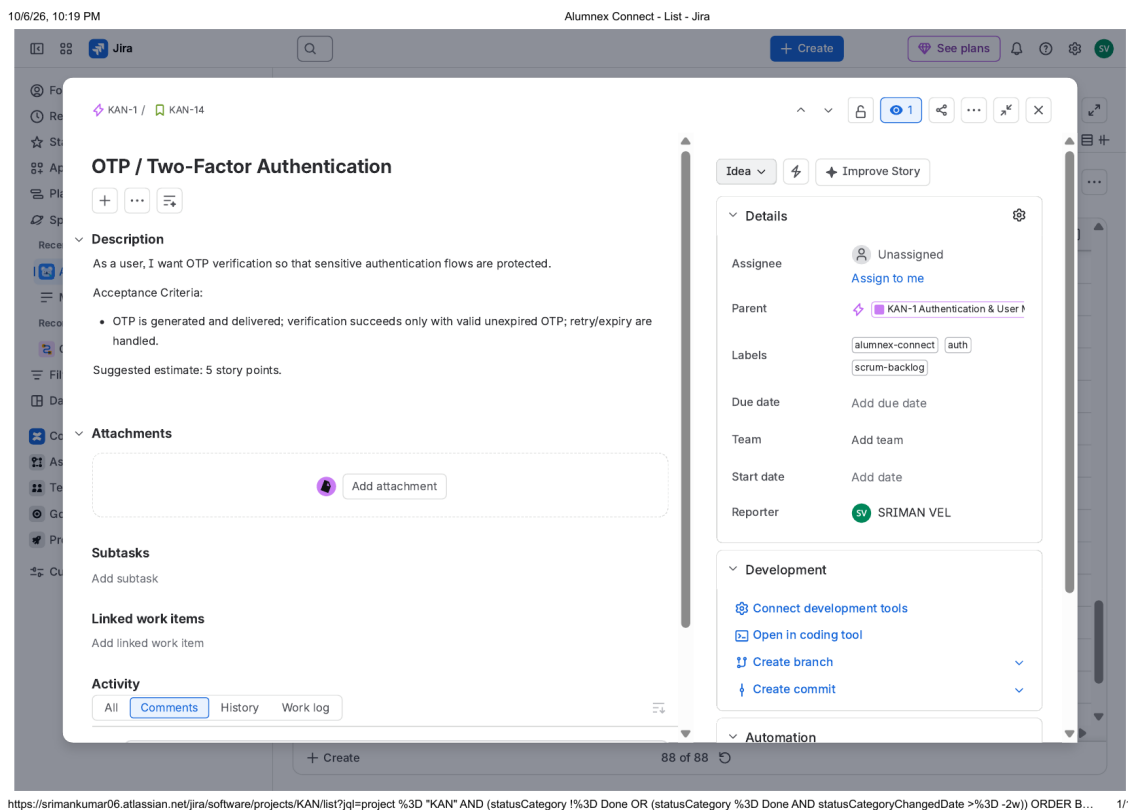


Figure 4. Jira Story detail example (KAN-14 OTP / Two-Factor Authentication) showing user story text, acceptance criteria, estimate, parent Epic and project labels.

For example, KAN-14 defines OTP behavior and explicitly states that valid, unexpired OTPs must succeed while retry and expiry handling must be supported. The Jira record also shows the parent Epic, labels, reporter and the suggested estimate. This is the level of detail expected for a refined backlog item.

8. Estimation and Story Points

All 53 Jira Stories contain a Suggested estimate value in the description. The distribution is 29 Stories at 5 points, 15 Stories at 3 points, 8 Stories at 8 points, and 1 Story at 2 points, giving a total of 256 suggested points. The supplied Story Point Baseline document explicitly states that these values are a planning baseline and not a claim of historical Sprint execution.

Alumnex Connect — Story Point Estimate Baseline

Alumnex Connect — Story Point Estimate Baseline

This page records the **Suggested estimate** values already embedded in the 53 Jira Story descriptions for project KAN. The estimates are a planning baseline, not a claim of historical Sprint execution.

Jira field constraint: the current KAN team-managed project does not expose a Story Points custom field in its issue-type metadata. The estimate values therefore remain documented in each story description and are consolidated here for reporting.

Baseline Summary

Metric	Value
Stories	53
Total suggested story points	256
Highest single estimate	8
Smallest estimate	2

Story-by-Story Register

Jira	Story	Epic	Phase	Points
KAN-11	Student Registration	Authentication & User Management	Phase 1 — Foundation	5
KAN-12	Student Login	Authentication & User Management	Phase 1 — Foundation	5
KAN-13	OAuth Authentication	Authentication & User Management	Phase 1 — Foundation	5

Figure 5. Story Point Estimate Baseline exported from Confluence/Jira documentation, showing the 53-story / 256-point baseline.

Jira configuration constraint: The KAN team-managed project does not expose a Story Points custom field in its issue-type metadata. The estimates are therefore retained in Story descriptions and in the baseline documentation instead of being represented as a nonexistent native field.

9. Board Workflow and Work-State Management

The board workflow is used as the project execution layer. Each state communicates where a work item is in its delivery lifecycle.

Board state	Operational meaning
Idea	Potential work or high-level capability not yet in execution
To Do	Refined work that is queued or awaiting execution
In Progress	Implementation actively underway
In Review	Testing, peer review or acceptance validation
Done	Work has passed the project quality/completion gate

9.1 Board population record

The board screenshot supplied at the beginning of the workflow showed 53 Story items in Idea, 5 Bugs in To Do, and zero board items in In Progress, In Review or Done. Subsequent Jira evidence shows the board populated across multiple workflow states. The current whole-project Jira Summary snapshot reports 88 total issues with 38 Done, 11 In Progress, 9 In Review, 20 To Do and 10 Idea; the 10 Idea issues are the Epic containers, while the board itself displays the 58 Story/Bug work items.

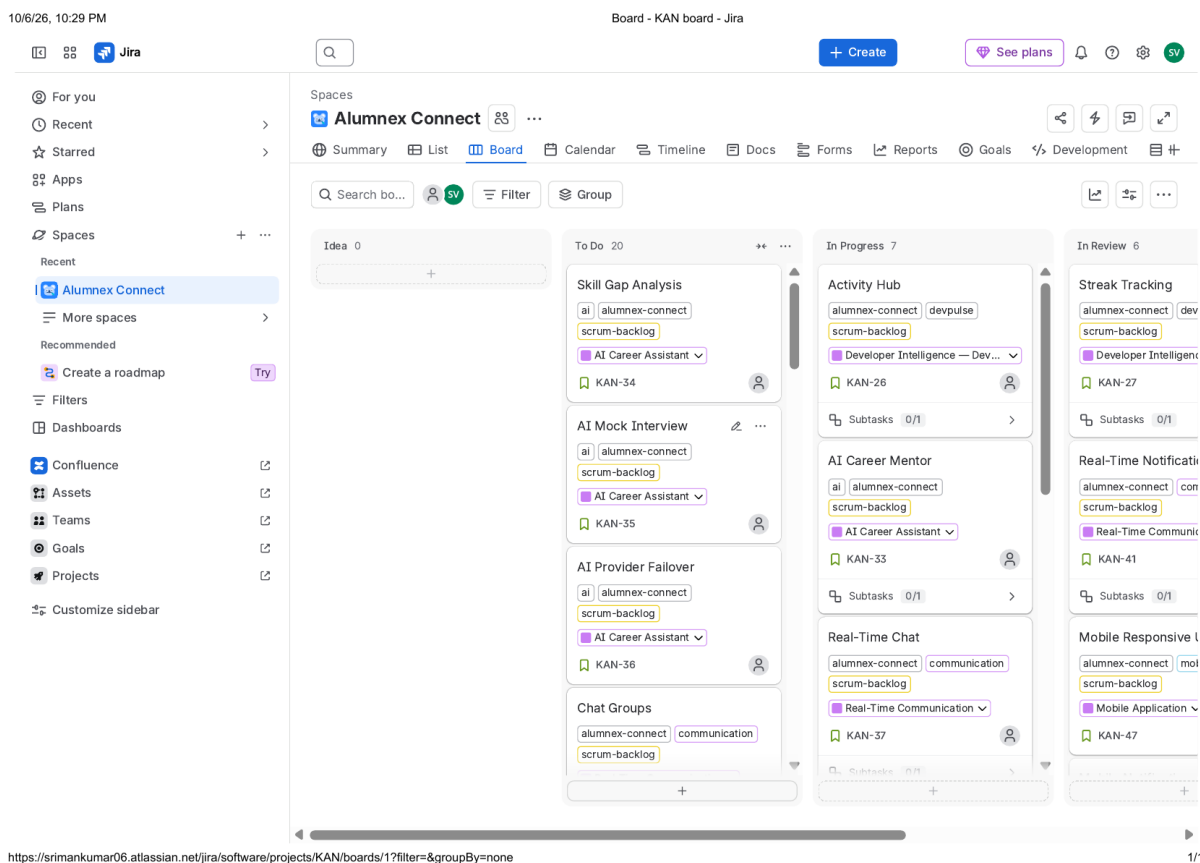


Figure 6. Jira Board evidence export after workflow population, showing To Do, In Progress and In Review work states; board work items are the executable Story/Bug layer.

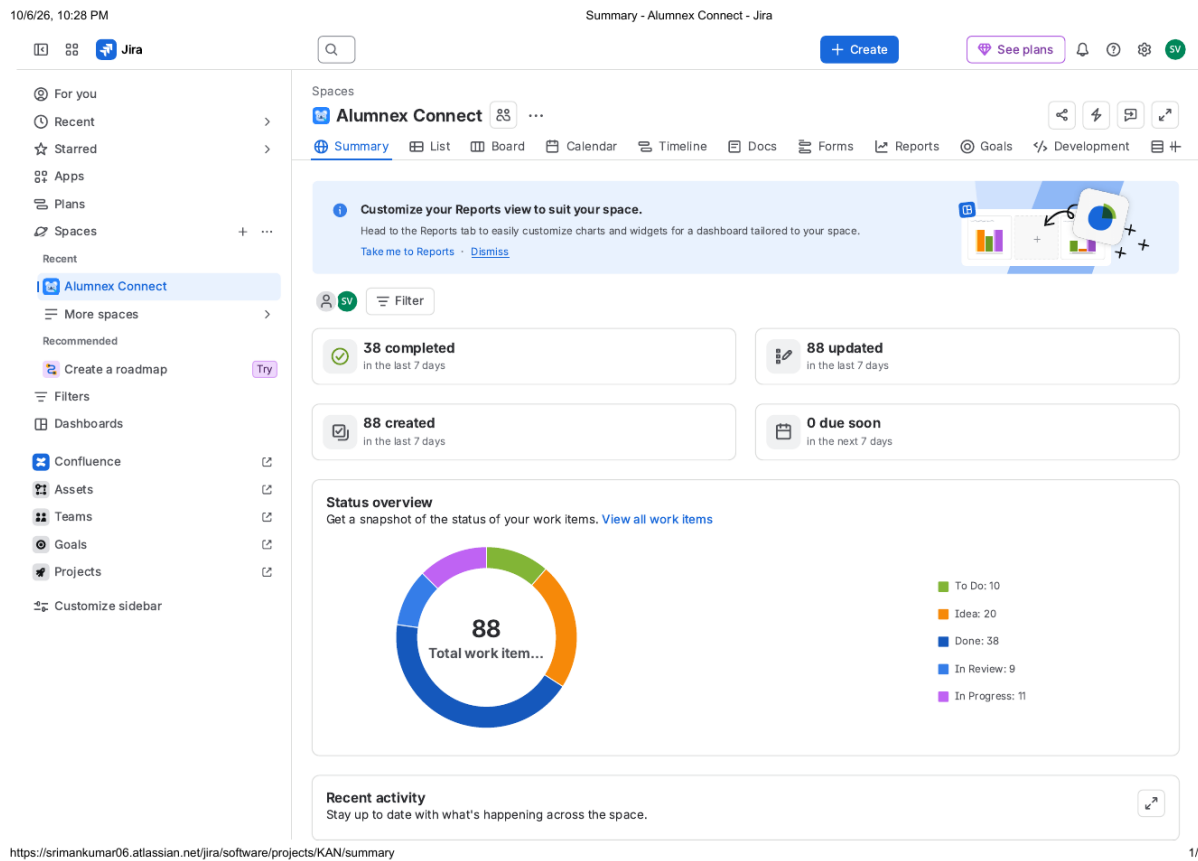


Figure 7. Jira Summary snapshot dated 06 October 2026 showing 88 total work items and the current distribution: 38 Done, 11 In Progress, 9 In Review, 20 To Do and 10 Idea.

Interpretation for an academic report: These status values are a current Jira management snapshot created to organize the project backlog and work-state view. They must not be presented as historical Sprint completion records.

10. Implementation Subtasks and Traceability

Twenty Subtasks were created so that implementation work can be connected to its parent Story. This is consistent with the practical Scrum reference, which recommends decomposing Stories into smaller technical tasks and then tracking their movement through the board.

Subtask	Work item	Parent Story
KAN-69	Design registration flow	KAN-11
KAN-70	Implement secure credential handling	KAN-11
KAN-71	Registration tests	KAN-11
KAN-72	Implement login flow	KAN-12
KAN-73	Handle authentication failures	KAN-12
KAN-74	Login tests	KAN-12
KAN-75	Mentor search and filters	KAN-17
KAN-76	Mentorship request workflow	KAN-18
KAN-77	Mentorship request tests	KAN-18
KAN-78	GitHub integration	KAN-22
KAN-79	Activity aggregation	KAN-26

KAN-80	Streak calculation	KAN-27
KAN-81	Resume PDF extraction	KAN-32
KAN-82	ATS scoring	KAN-32
KAN-83	AI chat integration	KAN-33
KAN-84	Socket messaging	KAN-37
KAN-85	Notification deduplication	KAN-41
KAN-86	Android wrapper	KAN-45
KAN-87	FCM registration	KAN-48
KAN-88	Security review	KAN-50

10/6/26, 10:18 PM Alumnex Connect - List - Jira

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Alumnex Connect

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Confluence

Assets

Teams

Goals

Projects

Customize sidebar

Spaces

Alumnex Connect

Summary List Board Calendar Timeline Docs Forms Reports Goals Development

Ask AI Search w... Filter 2 Group

Work	Assignee	Reporter	Priority
☐ KAN-10 Scrum & Project Governance	Unassigned	SV SRIMAN VEL	High
☐ KAN-9 Security, Reliability & DevOps	Unassigned	SV SRIMAN VEL	High
☐ KAN-8 Mobile Application	Unassigned	SV SRIMAN VEL	High
☐ KAN-7 Community & Events	Unassigned	SV SRIMAN VEL	High
☐ KAN-6 Real-Time Communication	Unassigned	SV SRIMAN VEL	High
☐ KAN-5 AI Career Assistant	Unassigned	SV SRIMAN VEL	High
☐ KAN-4 Career & Job Management	Unassigned	SV SRIMAN VEL	High
☐ KAN-3 Developer Intelligence — DevPulse	Unassigned	SV SRIMAN VEL	High
☐ KAN-2 Alumni-Student Mentorship	Unassigned	SV SRIMAN VEL	High
☐ KAN-1 Authentication & User Management	Unassigned	SV SRIMAN VEL	High
☐ KAN-68 Google Calendar Scope Access Denied	Unassigned	SV SRIMAN VEL	Medium
☐ KAN-66 Google OAuth Redirect URI Mismatch	Unassigned	SV SRIMAN VEL	High
☐ KAN-65 FCM Push Notification Delivery Failure	Unassigned	SV SRIMAN VEL	High
☐ KAN-64 Duplicate Reminder Notifications	Unassigned	SV SRIMAN VEL	High
☐ KAN-64 Daily Goal / Streak Synchronization Loss	Unassigned	SV SRIMAN VEL	High

+ Create 88 of 88

[https://srimankumar06.atlassian.net/jira/software/projects/KAN/list?ql=project %3D "KAN" AND %28statusCategory %21%3D Done OR %28statusCategory %3D Done AND statusCategoryChangedDate %3E%3D -2w%...](https://srimankumar06.atlassian.net/jira/software/projects/KAN/list?ql=project%3D%20KAN%20AND%20statusCategory%20%3D%20Done%20OR%20statusCategory%3D%20Done%20AND%20statusCategoryChangedDate%3E%3D%20-2w%20ago) 1/1

Figure 8. Jira List view showing implementation Subtasks and their traceable work items.

11. Release and Phase Management

Five Jira Versions were created to group work into coherent delivery phases. This creates a roadmap/release layer above the individual Story workflow.

Jira Version	Scope
Phase 1 - Foundation	Authentication, profiles, RBAC and platform foundation.
Phase 2 - Mentorship & Career	Mentorship workflows, jobs, applications and ATS.
Phase 3 - DevPulse	Developer integrations, activity hub and streak tracking.
Phase 4 - AI & Communication	AI career capabilities, chat and notifications.
Phase 5 - Mobile & Reliability	Mobile experience, security, failover, testing and monitoring.

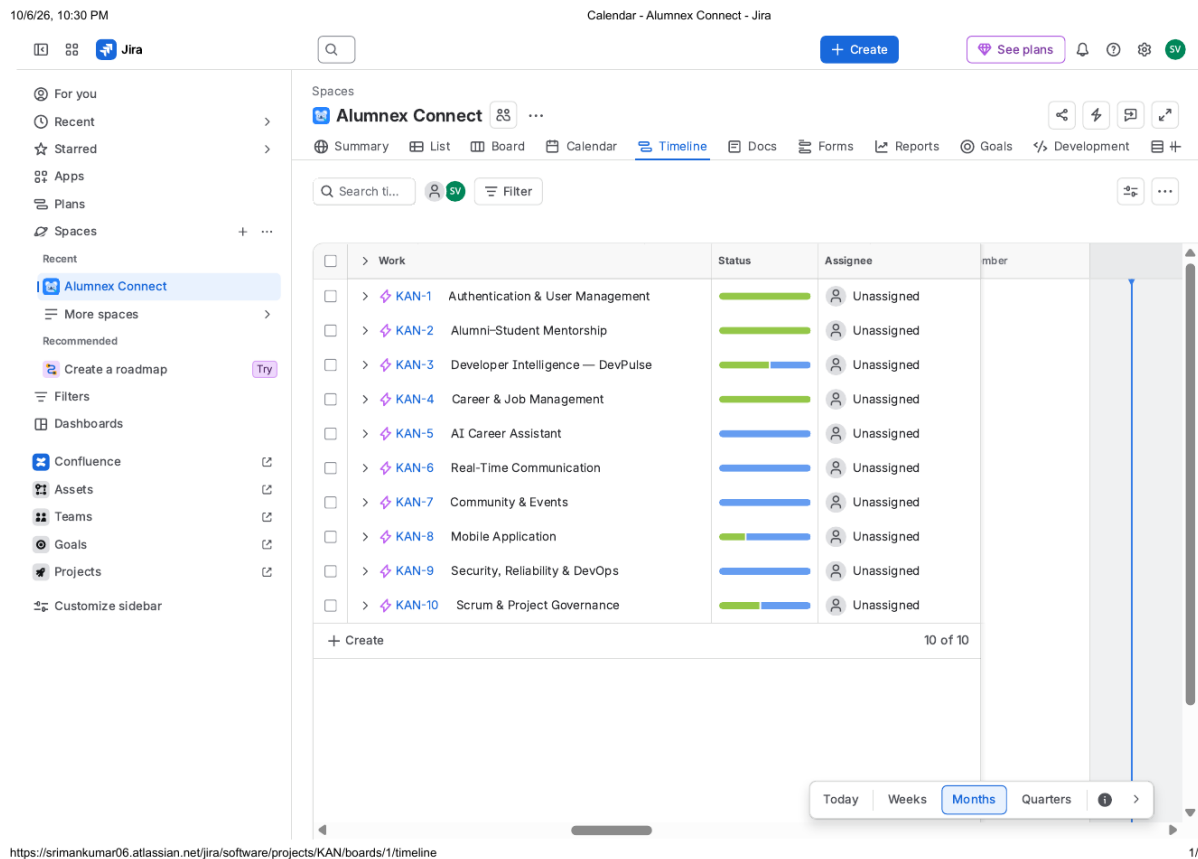


Figure 9. Jira Timeline view displaying the Epic-level product structure across the project roadmap.

In Agile terms, Versions are useful for release planning, while Sprints (when available) are time-boxed iteration contexts. The current KAN configuration provides the release-phase layer but not native Scrum Sprint execution.

12. Calendar and Scheduling View

The Calendar view provides a date-based perspective for work planning. The evidence export shows unscheduled work and makes it possible to assign due dates by dragging work items onto calendar dates. This supports scheduling and coordination, but does not by itself create a Sprint.

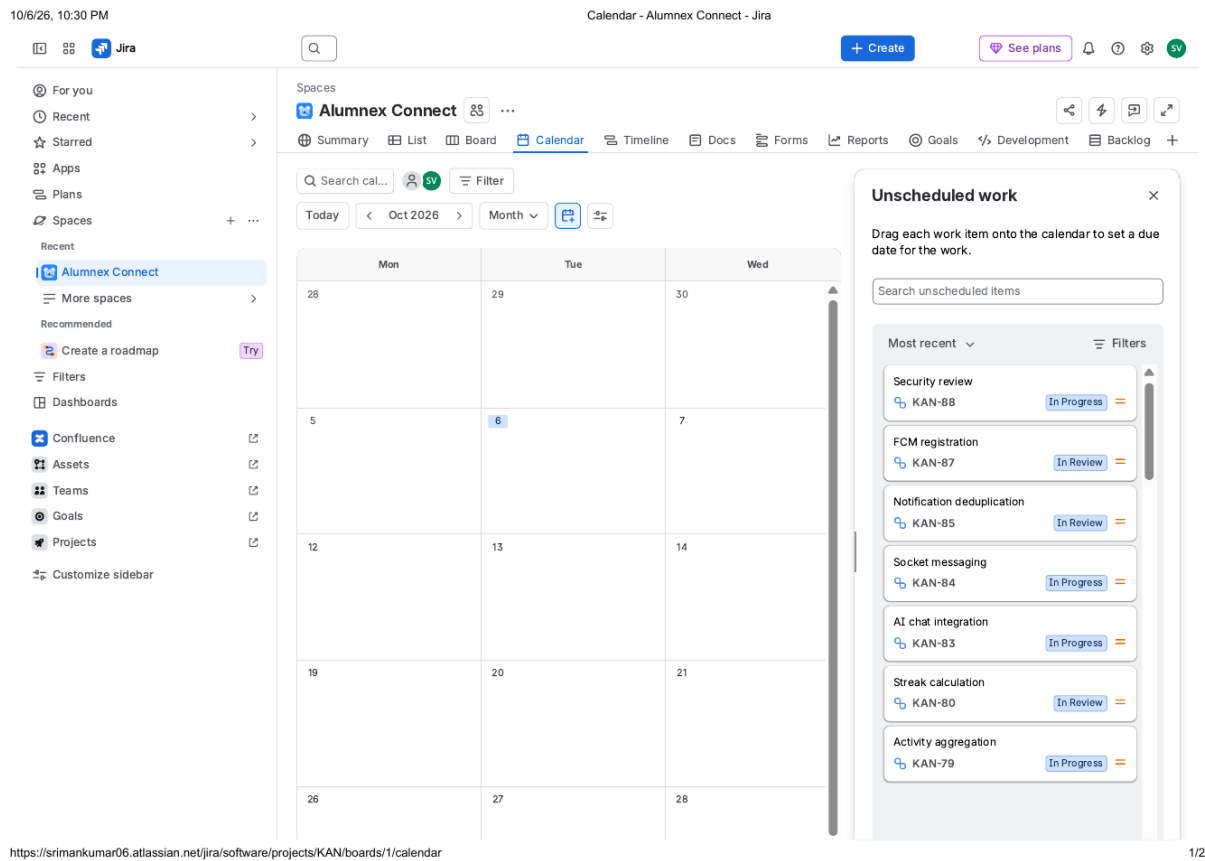


Figure 10. Jira Calendar view showing unscheduled work and work-state information.

13. Dependency Management

Eight issue links of type Blocks were created to make sequencing and risk visible. Dependency tracking is important because a technically valid Story may still be unable to progress until an upstream capability is available.

Source	Relationship	Target
KAN-33	blocks	KAN-36
KAN-45	blocks	KAN-46
KAN-48	blocks	KAN-66
KAN-26	blocks	KAN-64
KAN-41	blocks	KAN-65
KAN-13	blocks	KAN-67
KAN-33	blocks	KAN-68
KAN-50	blocks	KAN-52

Refinement note: During future backlog refinement, every Blocks relationship should be revalidated. If a relationship is informational rather than a hard sequencing constraint, a Relates link is more accurate than Blocks.

14. Defect Management

The project contains five observed/reported defects. Their descriptions include an observed problem statement, fix/acceptance criteria and a verification note. This is consistent with the supplied Scrum reference, which treats Bugs as visible work that progresses through an engineering lifecycle rather than being hidden outside the backlog.

Bug	Problem	Area	Fix / acceptance intent
KAN-64	Daily Goal / Streak Synchronization Loss	DevPulse	Persist goal completion, reconcile missed events, idempotent sync, expose last-sync timestamp.
KAN-65	Duplicate Reminder Notifications	Communication	Deduplicate by notification/event ID, coordinate delivery channels and add delivery logging.
KAN-66	FCM Push Notification Delivery Failure	Mobile	Validate FCM token lifecycle, credentials, retries and safe delivery logging.
KAN-67	Google OAuth Redirect URI Mismatch	Authentication	Align authorized redirect URIs with the active backend callback configuration.
KAN-68	Google Calendar Scope Access Denied	Career / Calendar	Review scopes and consent configuration, handle denial gracefully and document requirements.

All five Bugs are currently in To Do. They are explicitly marked in Jira as observed/reported defects and should be verified against the current implementation before being closed.

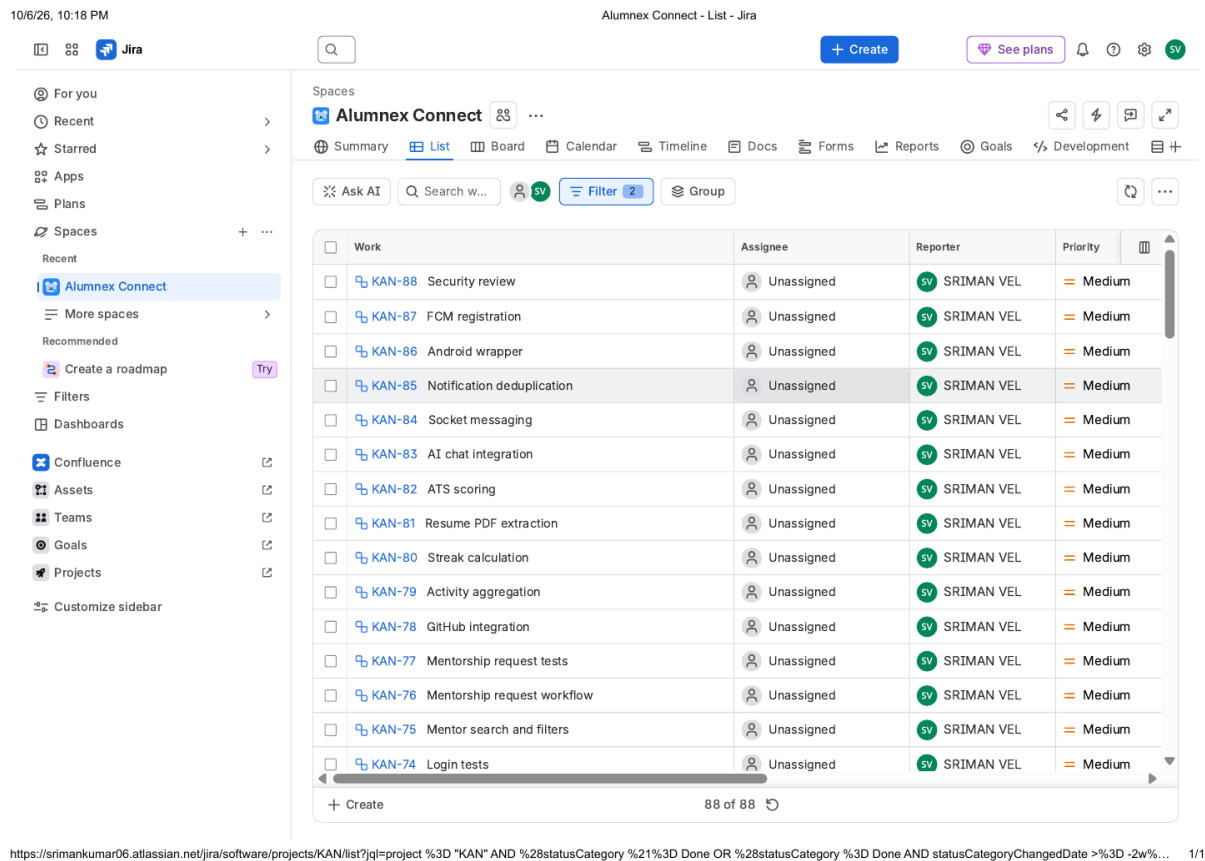


Figure 11. Jira List view showing the project work-item register, including Subtasks and reported Bugs.

15. Scrum Governance and Ceremonies

The governance layer is represented by KAN-55 through KAN-63 under the Scrum & Project Governance Epic. These issues define how a Scrum-style operating model would be run around the existing backlog.

Jira Story	Ceremony / governance practice	Application
KAN-55	Product Backlog & Refinement	Maintain clear outcomes, acceptance criteria and priorities.
KAN-56	Sprint Planning	Define Sprint Goal, selected work, estimates and capacity.
KAN-57	Daily Scrum Tracking	Inspect progress, blockers and plan adjustments.
KAN-58	Sprint Review & Stakeholder Feedback	Demonstrate increments and capture feedback.
KAN-59	Sprint Retrospective & Improvement Actions	Convert lessons into actionable improvements.
KAN-60	Definition of Ready & Definition of Done	Establish readiness and completion quality gates.
KAN-61	Risk, Dependency & Decision Tracking	Make important project constraints visible and traceable.
KAN-62	Release & Version Tracking	Connect backlog scope to delivery phases.
KAN-63	Agile Metrics & Continuous Improvement	Use delivery data for system improvement.

The practical Scrum reference also identifies roles such as Product Owner, Scrum Master, Developers and Tester. For Alumnex Connect, those roles are used as a process model; the connected Jira exports do not by themselves provide historical meeting attendance or role-assignment records, so this report does not invent such evidence.

15.1 Confluence documentation templates and where they fit

Template	Main content	Agile application
Project plan template	Driver, approver, contributors, objective, scope, timeline, milestones and status.	Project initiation, release planning and stakeholder alignment.
Meeting notes template	Date, participants, goals, discussion topics, action items, decisions and related information.	Daily Scrum, Sprint Planning, Review, Retrospective and stakeholder meetings.
Weekly status report template	Wins, needs input, focus, notes and important links.	Weekly stakeholder communication and management reporting.

16. Definition of Ready and Definition of Done

16.1 Definition of Ready (DoR)

- The user outcome is clear and valuable.
- Acceptance criteria are testable.
- Dependencies are known or explicitly tracked.
- Scope is small enough for the intended iteration.
- The team can explain what evidence will demonstrate success.

16.2 Definition of Done (DoD)

- Implementation is complete against the Story scope.
- Acceptance criteria are satisfied.
- Relevant automated/manual tests are completed.
- Code or implementation review is completed where applicable.
- Security/privacy considerations are addressed where relevant.
- Release/deployment requirements are satisfied when applicable.
- Required documentation is updated.

Agile application: DoR protects the quality of work entering execution; DoD protects the quality of work leaving execution. Together they create explicit quality gates rather than relying on a status label alone.

17. Jira Reporting, Metrics and Evidence

Jira provides Summary, Reports, Calendar, Timeline and Development views. The uploaded evidence demonstrates how the project can be reviewed from several angles rather than relying only on a board.

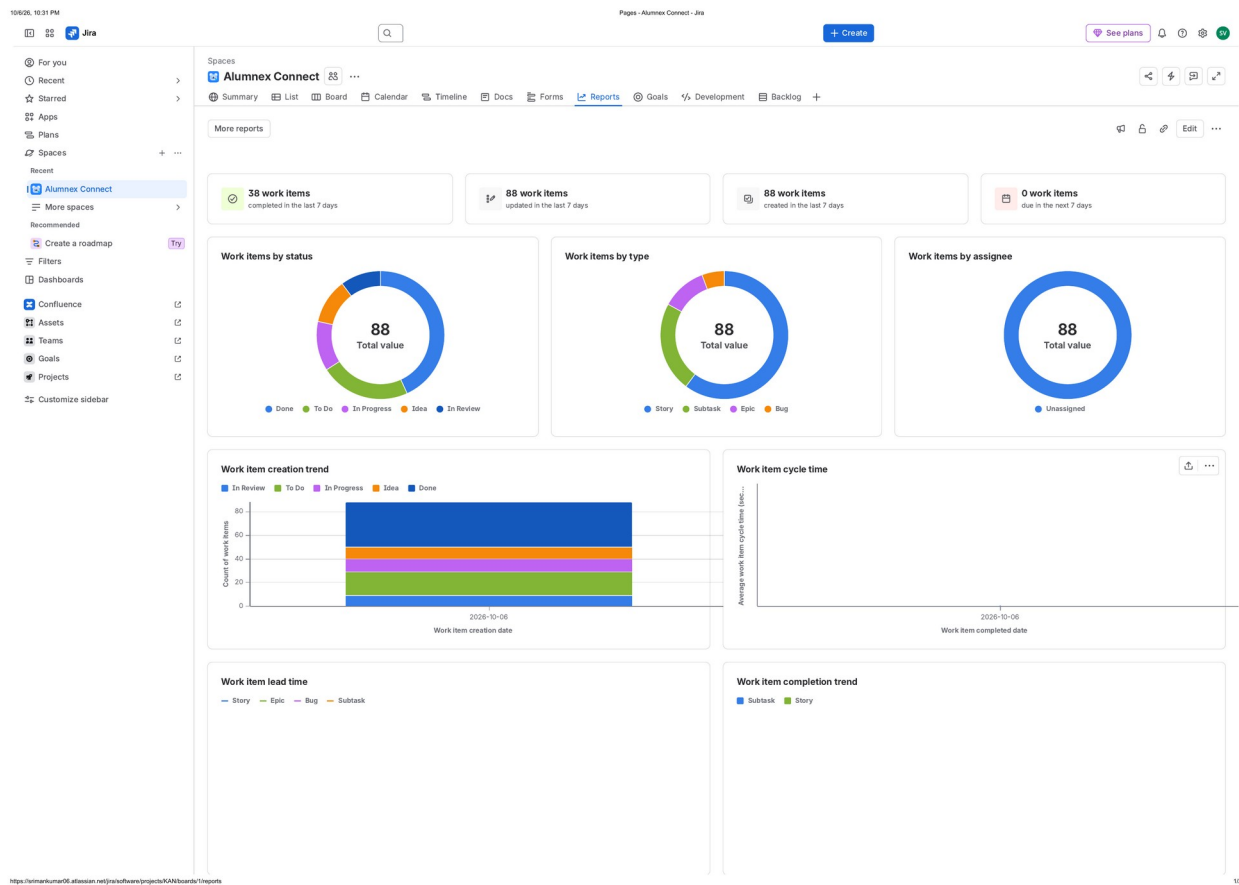


Figure 12. Jira Reports view showing work-item counts by status, type, assignee and trend-based views.

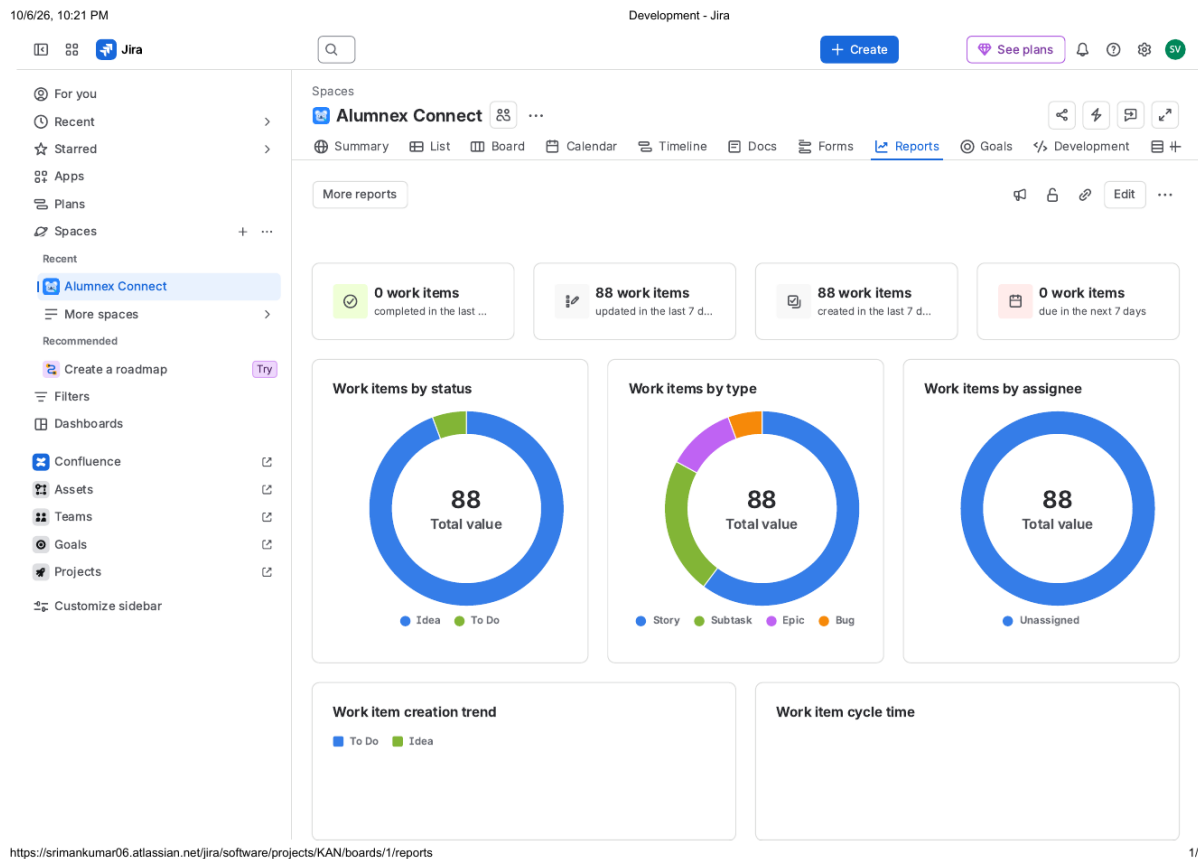


Figure 13. Jira Development view showing development connections and delivery metrics area.

The Reports evidence dated 06 October 2026 shows 38 work items completed in the last 7 days and 88 work items created/updated in that same period. Because the project-management structure was established in this period, these values primarily document Jira setup and state management rather than a historical product velocity.

Recommended Agile metrics for future real iterations are throughput, cycle time, work-item age, WIP, defect trends, release readiness and, after real Scrum Sprints exist, Sprint velocity and planned-versus-completed work.

18. Confluence Documentation and Knowledge Management

Confluence complements Jira by storing the narrative project-management layer. The dedicated Alumnex Connect Jira Project Management & Agile Playbook states that Jira is the source of truth for backlog, work status, defects, dependencies, releases and delivery metrics, while the playbook documents the Scrum model, backlog refinement, Sprint Planning, Daily Scrum, Sprint Review, Retrospective, DoR/DoD, risk/dependency tracking, release tracking and Agile metrics.

Alumnex Connect — Jira Project Management & Agile Playbook

Alumnex Connect Jira project-management and Agile/Scrum operating playbook.

Jira is the source of truth for backlog, work status, defects, dependencies, releases and delivery metrics.

Scrum model

- Product Backlog and refinement
- Sprint Planning
- Daily Scrum
- Sprint Review
- Sprint Retrospective
- Definition of Ready / Definition of Done
- Risk, dependency and decision tracking
- Release and version tracking
- Agile metrics and continuous improvement

Product areas

Authentication & User Management; Alumni–Student Mentorship; Developer Intelligence — DevPulse; Career & Job Management; AI Career Assistant; Real-Time Communication; Community & Events; Mobile Application; Security, Reliability & DevOps; Scrum & Project Governance.

Defect lifecycle

Record reproducible defects with observed behavior, expected behavior, impact, acceptance/fix criteria and verification notes. Do not close without validation.

Important configuration note

The current KAN board is a simple/team-managed board and does not support Jira Scrum sprints. Therefore no historical or active sprint records are being fabricated. The Scrum backlog and governance model are represented in Jira now; a Scrum-capable board can later use the same backlog for real Jira Sprints.

Reconstruction note

Because Alumnex Connect is already developed and the Jira project previously contained no issues, the created backlog and governance artifacts are a structured

Figure 14. Confluence Agile/Scrum playbook used as the project-management documentation layer.

19. How Agile Methodologies Apply to Alumnex Connect

Artifact / practice	Methodology	Jira evidence	Why it matters
Product Backlog	Scrum	KAN-11 to KAN-63 plus Bugs and Subtasks	Defines and prioritizes the work that can deliver product

			value.
Epic hierarchy	Scrum / Agile	KAN-1 to KAN-10	Groups large capability areas into manageable product outcomes.
User Stories	Scrum / Agile	53 Stories	Express work from the user perspective and create vertical increments.
Acceptance Criteria	Scrum / quality	Story descriptions	Create observable completion conditions for testing and review.
Subtasks	Agile / engineering	KAN-69 to KAN-88	Break implementation into smaller technical activities.
Workflow board	Kanban	KAN board	Makes flow, WIP and review stages visible.
Story estimates	Scrum / planning	Suggested estimates in 53 Stories	Support relative sizing; future Sprints can use them after native point support exists.
Bugs	Agile quality	KAN-64 to KAN-68	Treat defects as visible work with fix criteria and verification.
Versions	Release planning	Five Phase Versions	Organize delivery scope by release/phase.
Dependencies	Lean / Scrum planning	8 Blocks links	Surface sequencing risk and prevent hidden blockers.
DoR / DoD	Scrum	KAN-60	Control readiness and completion quality.
Retrospective	Scrum / continuous improvement	KAN-59	Convert experience into process improvements.
Automated testing / CI-CD	XP	KAN-52 / KAN-53	Reduce regression risk and shorten feedback loops.
Metrics	Kanban / Lean / Scrum	KAN-63 + Jira Reports	Use evidence to improve flow and planning.

20. Project Execution Record

The following sequence records the Jira-based project-management actions represented in the current workspace. It is intended as an auditable management log, not as a claim that every action occurred historically on the same date as the original software-development work.

Step	Execution record
1	Project structure established: Alumnex Connect / KAN project and KAN board verified.
2	Epic layer created: 10 product capability Epics created to organize the solution.
3	Story backlog built: 53 user Stories created with user-oriented descriptions and acceptance criteria.
4	Implementation decomposition: 20 Subtasks created for selected Stories.
5	Defect visibility: 5 observed/reported Bugs created with fix/acceptance criteria.
6	Release grouping: 5 Jira Versions created and non-Epic work assigned to the relevant phase.
7	Dependencies: 8 Blocks relationships recorded between related work items.
8	Workflow population: Stories/Subtasks were distributed across To Do, In Progress, In Review and Done to create a meaningful current work-state view.
9	Estimation baseline: 53 suggested Story estimates

	consolidated into a 256-point planning baseline.
10	Governance documentation: KAN-55 to KAN-63 and the Confluence Agile/Scrum playbook established the operating model.
11	Evidence capture: Backlog, Board, Summary, Calendar, Timeline, Reports, Development and Story-detail views exported for evidence.
12	Academic documentation: This report consolidates the project-management record and explains the Agile methodology mapping.

20.1 Current project status snapshot

Measure	Current value	Interpretation
Whole Jira project	88 issues	10 Epics, 53 Stories, 20 Subtasks, 5 Bugs
Whole-project status	38 Done / 11 In Progress / 9 In Review / 20 To Do / 10 Idea	Includes Epics and Subtasks
Board work-item layer	58 displayed Stories/Bugs	25 Done / 7 In Progress / 6 In Review / 20 To Do / 0 Idea
Release phases	5	Phase 1 to Phase 5
Suggested Story Points	256	53 Stories

21. Challenges, Constraints and Academic Reporting Rules

Constraint	Academic treatment
No native Scrum Sprint history	The KAN board is simple/team-managed and does not support native Jira Scrum Sprints. Therefore this report documents Scrum practices as an operating model, not as historical Sprint evidence.
No native Story Points field	The project metadata exposes no Story Points custom field. The 256-point baseline is retained in Story descriptions and documentation.
Observed Bugs require verification	The five Bugs are recorded from observed/reported behavior and should be re-tested against the current implementation before closure.
Dependency semantics	The eight Blocks links should be revalidated during future refinement to ensure that each is truly a blocker.
Assignment evidence	The exported issue views show many items as Unassigned; this report does not invent individual responsibility assignments.
Jira metrics timing	The 06 October 2026 reports show recent creation/update activity because the project-management structure was established recently.

22. Results and Outcomes

- Created a structured Agile backlog with 10 Epics, 53 Stories, 20 Subtasks and 5 Bugs.
- Organized the product into five release/phase Versions.
- Established a visible flow-based Jira board with five workflow states.
- Created traceability between Stories and implementation Subtasks.
- Recorded observed defects with acceptance/fix criteria and verification notes.
- Established dependency visibility through issue links.
- Created a documented estimation baseline of 256 suggested Story Points.

- Added Scrum governance artifacts covering backlog refinement, planning, Daily Scrum, Review, Retrospective, DoR/DoD, risks, releases and metrics.
- Built a Confluence knowledge layer and captured Jira/Confluence UI evidence for the academic report.

23. Conclusion

The Alumnex Connect Jira workspace now provides a structured Agile project-management record connecting product capabilities, user requirements, implementation work, quality issues, release phases, dependencies and governance. The board provides a clear flow-based work view, while Confluence provides the supporting process documentation.

The strongest current methodological fit is a hybrid Agile model: Scrum governs how the backlog should be refined, planned, reviewed and improved; Kanban provides the actual visible workflow in the current team-managed Jira board; XP principles can strengthen engineering quality through automated testing and CI/CD; and Lean principles support waste reduction, short feedback loops and flow improvement.

For a future iteration in which native Scrum reporting is required, the project should be migrated or recreated in a Scrum-capable Jira configuration and the same backlog, acceptance criteria, Subtasks, Bugs and release structure can then be used to manage real time-boxed Sprints.

Appendix A - Complete Epic Register

KAN-1 - Authentication & User Management

Identity, registration, login, OAuth, OTP, profiles, RBAC

KAN-2 - Alumni-Student Mentorship

Mentor discovery, requests, sessions, reviews

KAN-3 - Developer Intelligence - DevPulse

Coding-platform integrations, activity hub and streaks

KAN-4 - Career & Job Management

Job posting, browsing, applications and ATS

KAN-5 - AI Career Assistant

AI mentor, skill-gap analysis, mock interview and failover

KAN-6 - Real-Time Communication

Chat, groups, presence, read receipts and notifications

KAN-7 - Community & Events

Forum, events and alumni networking

KAN-8 - Mobile Application

Android wrapper, mobile authentication, responsive UI and push

KAN-9 - Security, Reliability & DevOps

Security hardening, failover, testing, CI/CD, monitoring

KAN-10 - Scrum & Project Governance

Backlog, ceremonies, quality gates, risks, releases and metrics

Appendix B - Story Register

Jira	Story	Epic	Current status	Suggested points
KAN-11	Student Registration	KAN-1	Done	5
KAN-12	Student Login	KAN-1	Done	5
KAN-13	OAuth Authentication	KAN-1	Done	5
KAN-14	OTP / Two-Factor Authentication	KAN-1	Done	5
KAN-15	User Profile Management	KAN-1	Done	3
KAN-16	Role-Based Access Control	KAN-1	Done	5
KAN-17	Browse Alumni Mentors	KAN-2	Done	5
KAN-18	Request Mentorship	KAN-2	Done	5
KAN-19	Manage Mentorship Requests	KAN-2	Done	5
KAN-20	Mentorship Session	KAN-2	Done	5

	Tracking			
KAN-21	Mentorship Reviews	KAN-2	Done	3
KAN-22	GitHub Developer Statistics	KAN-3	Done	5
KAN-23	LeetCode Statistics	KAN-3	Done	5
KAN-24	Codeforces Statistics	KAN-3	Done	5
KAN-25	Unified Developer Profile	KAN-3	Done	3
KAN-26	Activity Hub	KAN-3	In Progress	8
KAN-27	Streak Tracking	KAN-3	In Review	5
KAN-28	Job Posting	KAN-4	Done	5
KAN-29	Browse Job Opportunities	KAN-4	Done	5
KAN-30	Apply for Jobs	KAN-4	Done	5
KAN-31	Job Application Management	KAN-4	Done	5
KAN-32	ATS Resume Analysis	KAN-4	Done	8
KAN-33	AI Career Mentor	KAN-5	In Progress	8
KAN-34	Skill Gap Analysis	KAN-5	To Do	8
KAN-35	AI Mock Interview	KAN-5	To Do	8
KAN-36	AI Provider Failover	KAN-5	To Do	5
KAN-37	Real-Time Chat	KAN-6	In Progress	8
KAN-38	Chat Groups	KAN-6	To Do	5
KAN-39	Online Presence	KAN-6	To Do	3
KAN-40	Read Receipts	KAN-6	To Do	3
KAN-41	Real-Time Notifications	KAN-6	In Review	5
KAN-42	Community Forum	KAN-7	To Do	5
KAN-43	Event Management	KAN-7	To Do	5
KAN-44	Alumni Networking	KAN-7	To Do	5
KAN-45	Android Mobile Wrapper	KAN-8	Done	8
KAN-46	Mobile Authentication	KAN-8	In Progress	5
KAN-47	Mobile Responsive UI	KAN-8	In Review	5
KAN-48	Mobile Notifications	KAN-8	In Review	5
KAN-49	Android APK Build & Release	KAN-8	To Do	3
KAN-50	Security Hardening	KAN-9	In Progress	8
KAN-51	API Failover	KAN-9	To Do	5
KAN-52	Automated Testing	KAN-9	In Review	5
KAN-53	CI/CD Pipeline	KAN-9	To Do	5
KAN-54	Production Monitoring	KAN-9	To Do	3
KAN-55	Product Backlog & Refinement	KAN-10	Done	3
KAN-56	Sprint Planning	KAN-10	Done	3
KAN-57	Daily Scrum Tracking	KAN-10	In Progress	2
KAN-58	Sprint Review & Stakeholder Feedback	KAN-10	To Do	3
KAN-59	Sprint Retrospective & Improvement Actions	KAN-10	To Do	3
KAN-60	Definition of Ready & Definition of Done	KAN-10	Done	3
KAN-61	Risk, Dependency & Decision Tracking	KAN-10	In Progress	3
KAN-62	Release & Version Tracking	KAN-10	Done	3
KAN-63	Agile Metrics & Continuous Improvement	KAN-10	In Review	3

Appendix C - Subtask Register

Jira	Subtask	Parent Story	Current status
KAN-69	Design registration flow	KAN-11	Done
KAN-70	Implement secure credential handling	KAN-11	Done
KAN-71	Registration tests	KAN-11	Done
KAN-72	Implement login flow	KAN-12	Done
KAN-73	Handle authentication failures	KAN-12	Done
KAN-74	Login tests	KAN-12	Done
KAN-75	Mentor search and filters	KAN-17	Done
KAN-76	Mentorship request workflow	KAN-18	Done
KAN-77	Mentorship request tests	KAN-18	Done
KAN-78	GitHub integration	KAN-22	Done
KAN-79	Activity aggregation	KAN-26	In Progress
KAN-80	Streak calculation	KAN-27	In Review
KAN-81	Resume PDF extraction	KAN-32	Done
KAN-82	ATS scoring	KAN-32	Done
KAN-83	AI chat integration	KAN-33	In Progress
KAN-84	Socket messaging	KAN-37	In Progress
KAN-85	Notification deduplication	KAN-41	In Review
KAN-86	Android wrapper	KAN-45	Done
KAN-87	FCM registration	KAN-48	In Review
KAN-88	Security review	KAN-50	In Progress

Appendix D - Bug Register

Bug	Summary	Area	Current status	Priority
KAN-64	Daily Goal / Streak Synchronization Loss	DevPulse	To Do	High
KAN-65	Duplicate Reminder Notifications	Communication	To Do	High
KAN-66	FCM Push Notification Delivery Failure	Mobile	To Do	High
KAN-67	Google OAuth Redirect URI Mismatch	Authentication	To Do	High
KAN-68	Google Calendar Scope Access Denied	Career / Calendar	To Do	Medium

Appendix E - Screenshot Evidence Log

Figure	Screen	Evidence source	What it proves
Figure 1	Jira Backlog - page 1	Alumnex Connect - Backlog - Jira.pdf	Evidence of backlog structure and Epic/Story grouping.
Figure 2	Jira Backlog - page 2	Alumnex Connect - Backlog - Jira.pdf	Continued Story register.
Figure 3	Jira Board before workflow population	User-provided screenshot	Initial state: 53 Stories in Idea, 5 Bugs in To Do.
Figure 4	Jira Story detail	Alumnex Connect - 2FA- Jira.pdf	Story structure, Acceptance Criteria, estimate, parent Epic and labels.
Figure 5	Story Point baseline	MFS-Alumnex Connect - Story Point Estimate Baseline PDF	53 Stories and 256 suggested points.
Figure 6	Jira Board workflow	Board - KAN board - Jira.pdf	Visible To Do, In Progress and In Review flow states.
Figure 7	Jira Summary	Summary - Alumnex Connect - Jira.pdf	88 total work items and current status distribution.
Figure 8	Jira List / implementation register	Alumnex Connect - List2 - Jira.pdf	Subtasks and implementation work.
Figure 9	Jira Timeline	Timeline - Alumnex Connect - Jira.pdf	Epic-level roadmap view.
Figure 10	Jira Calendar	Calendar - Alumnex Connect - Jira.pdf	Date-based planning and unscheduled work.
Figure 11	Jira List	Alumnex Connect - List - Jira.pdf	Project issue register and visible tracking.
Figure 12	Jira Reports	Pages - Alumnex Connect - Jira.pdf	Status, work type, creation and completion reporting.
Figure 13	Jira Development	Development - Jira.pdf	Development connections and technical delivery metrics area.
Figure 14	Confluence Agile/Scrum playbook	MFS-Alumnex Connect - Jira Project Management & Agile Playbook PDF	Process, governance, quality and Agile documentation.

References

- 1. Practical Scrum Process Using Jira (uploaded reference document).** Used as the methodology/process reference for requirements, Stories, Epics, estimation, Sprint planning, task decomposition, Daily Scrum, testing, Bugs, Review, Retrospective and reporting.
- 2. Alumnex Connect - Jira Project Management & Agile Playbook (Confluence export).** Used as the project-specific governance source for Scrum model, quality gates, dependency management, releases and reporting.
- 3. Alumnex Connect - Story Point Estimate Baseline (Confluence export).** Used for the 53-story / 256-point planning baseline and the Story Points field constraint.
- 4. Alumnex Connect Jira UI exports: Backlog, Board, Summary, List, List2, Calendar, Timeline, Reports/Pages, Development and Story detail.** Used as direct visual evidence of the Jira workspace and its project-management configuration on 06 October 2026.
- 5. Confluence templates: Project plan, Meeting notes and Weekly status report.** Used to explain how project plans, meeting records and weekly reporting fit into Agile governance and stakeholder communication.
