

ALUMNEX CONNECT

JIRA-BASED AGILE PROJECT EXECUTION AND MANAGEMENT REPORT

Ready-to-Submit Project Documentation

Project	Alumnex Connect - Integrated Alumni-Student Mentorship and Career Ecosystem
Jira Project	Alumnex Connect (KAN)
Jira Board	KAN board
Agile Approach	Agile product management with Scrum governance and flow-based Jira workflow
Documentation Date	06 October 2026
Prepared For	Academic project review / viva / project documentation

Academic evidence note: This report documents the Jira project-management record and current workspace state. It does not claim that the current Jira workspace contains historical Scrum Sprint execution. The connected KAN board is a simple/team-managed board without native Jira Scrum Sprint history.

**Department of Computer Science and Engineering
Kongu Engineering College (Autonomous)**

Document Control

Item	Record
Document title	Alumnex Connect - Jira-Based Agile Project Execution and Management Report
Project identifier	KAN
Primary management tool	Jira Software / Alumnex Connect
Documentation repository	Confluence - My first space
Reporting basis	Connected Jira/Confluence workspace and uploaded Jira/Confluence evidence exports
Evidence date	06 October 2026
Status	Prepared for academic submission

Table of Contents

- 1. Executive Summary
- 2. Introduction and Project Context
- 3. Agile Methodology Adopted
- 4. Requirements-to-Jira Transformation
- 5. Jira Project Configuration
- 6. Product Backlog Structure
- 7. User Stories and Acceptance Criteria
- 8. Estimation and Story Points
- 9. Board Workflow and Work-State Management
- 10. Implementation Subtasks and Traceability
- 11. Release and Phase Management
- 12. Dependency Management
- 13. Defect Management
- 14. Scrum Governance and Ceremonies
- 15. Definition of Ready and Definition of Done
- 16. Jira Reporting, Metrics and Evidence
- 17. Confluence Documentation and Knowledge Management
- 18. How Agile Methodologies Apply to Alumnex Connect
- 19. Project Execution Record
- 20. Challenges, Constraints and Academic Reporting Rules
- 21. Results and Outcomes
- 22. Conclusion
- Appendix A - Epic Register
- Appendix B - Story Register
- Appendix C - Subtask Register
- Appendix D - Bug Register
- Appendix E - Screenshot Evidence Log
- References

1. Executive Summary

Alumnex Connect is an integrated alumni-student ecosystem containing authentication, mentorship, developer intelligence (DevPulse), career and jobs, AI career support, real-time communication, community, mobile access, and security/reliability capabilities. The Jira workspace was organized so that these capabilities can be managed as a coherent Agile product rather than as an unstructured list of features.

The verified Jira project contains 10 Epics, 53 Stories, 20 Subtasks and 5 Bugs, giving 88 Jira issues in total. Five Jira Versions divide the backlog into delivery phases. The workflow uses Idea, To Do, In Progress, In Review and Done. The uploaded Jira evidence and current connected Jira state show that the board has been populated across multiple work states rather than leaving all work in the initial backlog state.

The practical Scrum reference supplied for this report describes a flow from requirements gathering to backlog creation, Epic and Story decomposition, estimation, Sprint Planning, task/subtask execution, Daily Scrum, testing, bug fixing, Sprint Review, feedback, Retrospective and reporting. Those concepts have been mapped to Alumnex Connect, while the Jira configuration limits are explicitly separated from the Scrum process model.

Key project-management result: The report establishes a traceable management chain: product capability -> Epic -> user Story -> acceptance criteria -> implementation Subtask -> workflow state -> release phase -> dependency/defect evidence -> documentation and metrics.

2. Introduction and Project Context

2.1 Project context

Alumnex Connect is designed as an integrated digital ecosystem connecting students and alumni through mentorship, career opportunities, developer activity tracking, AI-assisted career guidance, communication, community participation and mobile access. The Jira backlog groups the product around these functional areas and adds a dedicated governance layer for Agile project management.

2.2 Project management objective

The objective of using Jira is to make work visible, decomposable, traceable and reviewable. Jira acts as the operational record for backlog items, status, defects, dependencies and release grouping; Confluence holds the narrative rules, ceremony guidance, quality gates and project knowledge.

2.3 Why Agile fits the project

The product contains multiple interacting capabilities, external integrations, mobile behavior, AI services and reliability concerns. An incremental Agile model is therefore useful because functionality can be broken into small deliverables, risks can be surfaced as visible work, feedback can be incorporated, and releases can be organized in phases.

3. Agile Methodology Adopted

The project is best described as an Agile implementation with four complementary lenses: Scrum for governance and iterative planning, Kanban for visible work flow, XP for engineering quality practices, and Lean for reducing waste and improving flow.

Methodology	How it contributes	Application in Alumnex Connect
Scrum	Product Backlog, Stories, estimates, Sprint Planning, Daily Scrum, Review, Retrospective, DoR and DoD.	Documented in KAN-55 to KAN-63 and the Confluence playbook; native Jira Sprints are not available on the current board.
Kanban	Visible workflow, WIP awareness, bottlenecks, cycle time and continuous flow.	Implemented directly through the KAN board workflow: Idea -> To Do -> In Progress -> In Review -> Done.
XP	Automated testing, CI/CD, continuous integration, small increments and engineering quality.	Represented by KAN-52 Automated Testing, KAN-53 CI/CD Pipeline and KAN-50 Security Hardening; specific historical XP practices require independent evidence.
Lean	Reduce waste, limit unnecessary handoffs, expose blockers, optimise value delivery and use feedback for improvement.	Supported by visible workflow, dependency links, release phases and the continuous-improvement governance item KAN-63.

3.1 Reference Scrum process used for mapping

The supplied Practical Scrum Process Using Jira document explains a complete example beginning with customer requirements, conversion into User Stories, Epic grouping, priority and Story Point estimation, Sprint creation, task/subtask decomposition, assignment, development, Daily Scrum, testing, bug lifecycle, Story completion, Sprint Review, customer feedback, Retrospective, Sprint completion and reporting. The same lifecycle is used in this report as the reference framework for explaining where each Alumnex Jira artifact fits.

4. Requirements-to-Jira Transformation

The first Agile transformation is from broad product requirements into manageable backlog items. Instead of maintaining all functionality as large feature statements, the project converts capabilities into Epics and then into user-value Stories.

Agile step	Alumnex Connect application
Requirement capture	Identify the user or business outcome to be delivered.
Epic grouping	Group related functionality into a coherent product capability.
User Story creation	Express a feature using the user/goal/benefit pattern.
Acceptance criteria	Define observable conditions that determine whether the Story is complete.
Estimation	Record a relative effort/complexity estimate.
Implementation decomposition	Create Subtasks for the technical work needed to satisfy the Story.
Workflow execution	Move work through the board as it is refined, developed and reviewed.
Quality and feedback	Track Bugs and review evidence before marking work complete.
Release grouping	Assign work to the appropriate delivery phase.

4.1 Evidence: Jira backlog

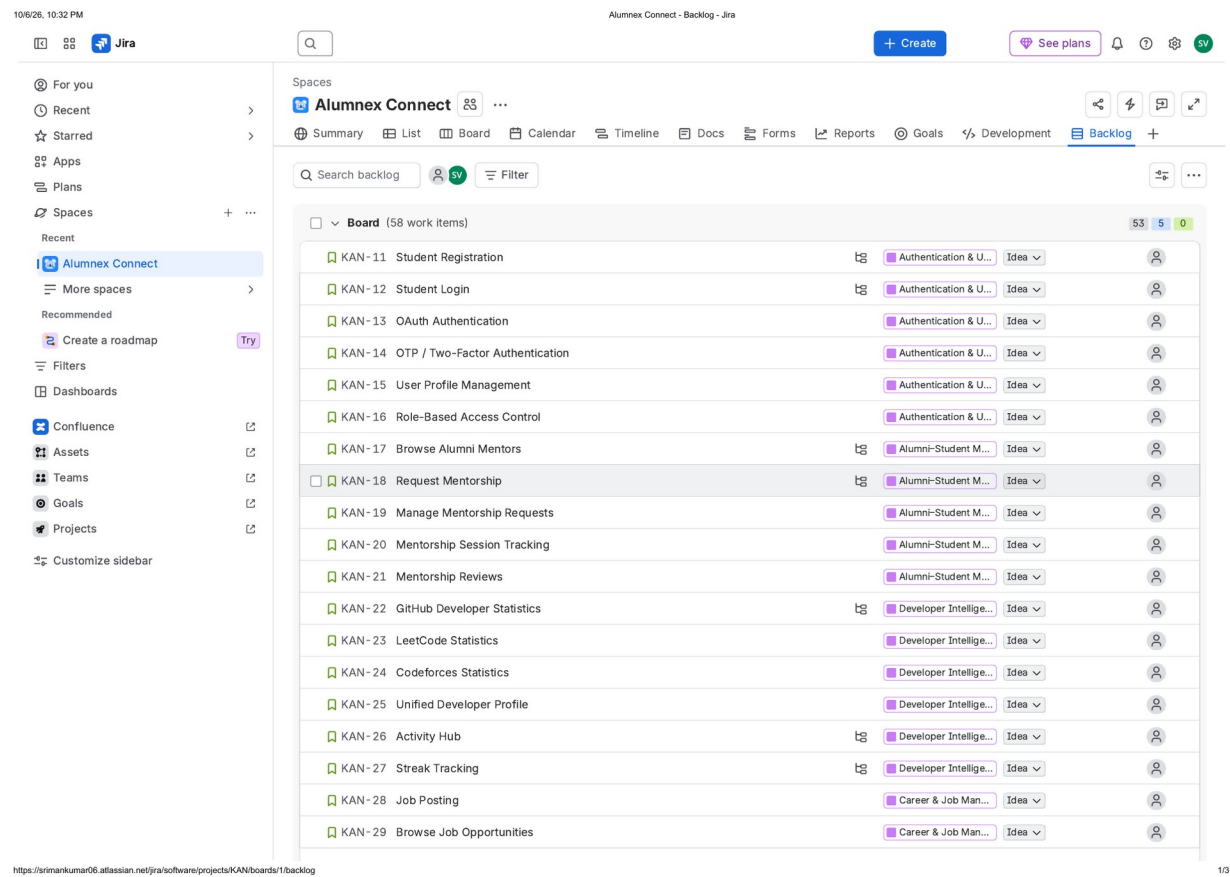


Figure 1. Jira Backlog view showing the Alumnex Connect backlog and grouped Epic/Story structure.

KAN - 30	Apply for Jobs	Career & Job Man...	Idea	▼	👤
KAN - 31	Job Application Management	Career & Job Man...	Idea	▼	👤
KAN - 32	ATS Resume Analysis	Career & Job Man...	Idea	▼	👤
KAN - 33	AI Career Mentor	AI Career Assistant	Idea	▼	👤
KAN - 34	Skill Gap Analysis	AI Career Assistant	Idea	▼	👤
KAN - 35	AI Mock Interview	AI Career Assistant	Idea	▼	👤
KAN - 36	AI Provider Failover	AI Career Assistant	Idea	▼	👤
KAN - 37	Real-Time Chat	Real-Time Commu...	Idea	▼	👤
KAN - 38	Chat Groups	Real-Time Commu...	Idea	▼	👤
KAN - 39	Online Presence	Real-Time Commu...	Idea	▼	👤
KAN - 40	Read Receipts	Real-Time Commu...	Idea	▼	👤
KAN - 41	Real-Time Notifications	Real-Time Commu...	Idea	▼	👤

Figure 2. Continued Jira Backlog view showing additional Alumnex Connect Stories.

5. Jira Project Configuration

The connected workspace identifies the project as Alumnex Connect (KAN) with a built-in board named KAN board. The board is a simple/team-managed configuration. The verified board columns are Idea, To Do, In Progress, In Review and Done.

Configuration item	Verified value
Project key	KAN
Project type	Team-managed / simple
Board	KAN board
Workflow	Idea -> To Do -> In Progress -> In Review -> Done
Issue types in the project	Epic, Story, Subtask, Bug
Jira Versions	5 delivery phases
Recorded dependency links	8 Blocks links
Confluence space	My first space (MFS)

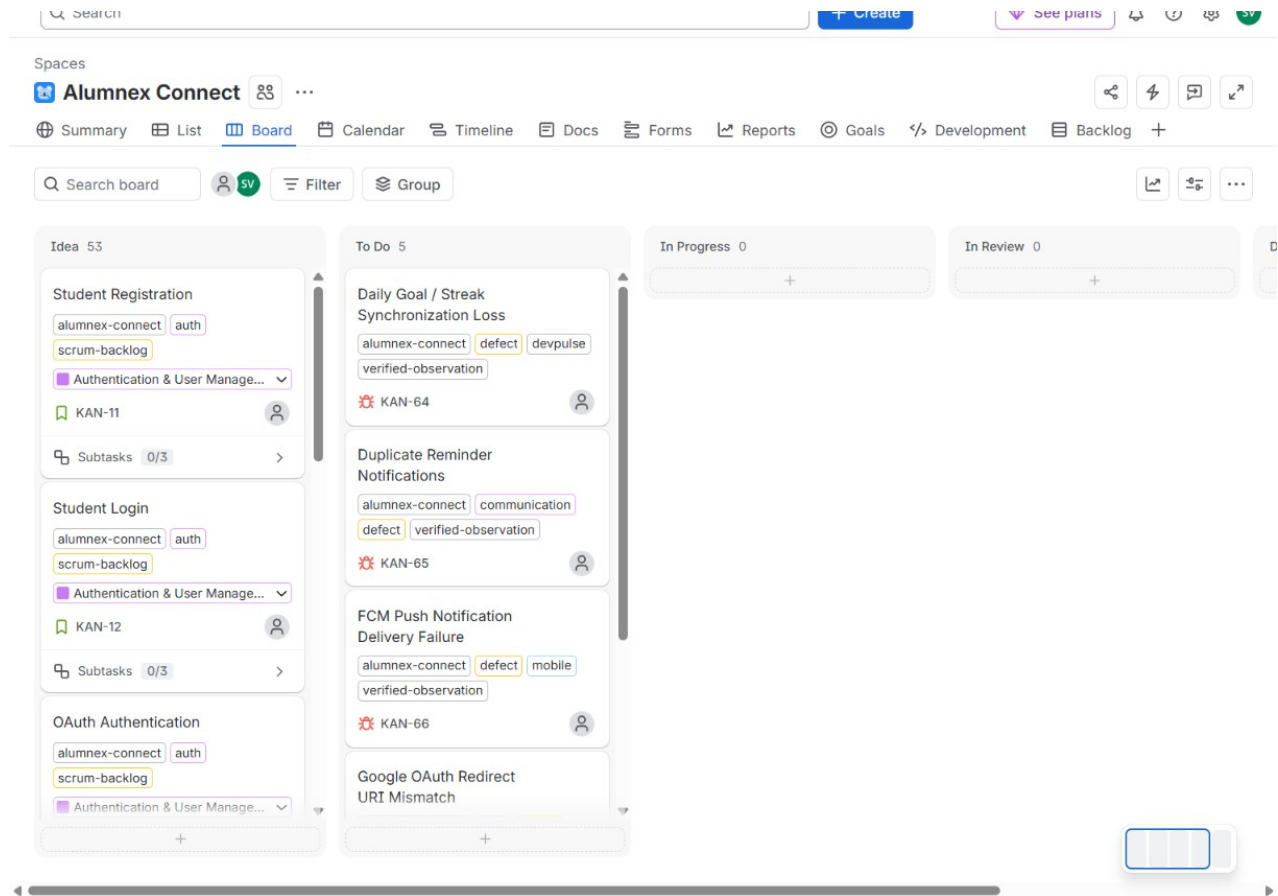


Figure 3. User-provided Jira Board screenshot before workflow population: 53 board Stories were in Idea and 5 Bugs were in To Do.

6. Product Backlog Structure

The backlog is organized into four principal issue layers. Epics provide the strategic capability boundary. Stories represent user-value increments. Subtasks represent implementation activities. Bugs represent quality deviations that require corrective work.

Issue type	Purpose	Agile role
Epic	Large capability or outcome	Roadmap and product structure
Story	User-visible outcome	Product Backlog and incremental delivery
Subtask	Concrete implementation activity	Development execution and traceability
Bug	Observed defect/deviation	Quality management and release readiness

6.1 Epic register

Key	Epic	Purpose
KAN-1	Authentication & User Management	Identity, registration, login, OAuth, OTP, profiles, RBAC
KAN-2	Alumni-Student Mentorship	Mentor discovery, requests, sessions, reviews
KAN-3	Developer Intelligence - DevPulse	Coding-platform integrations, activity hub and streaks
KAN-4	Career & Job Management	Job posting, browsing, applications and

		ATS
KAN-5	AI Career Assistant	AI mentor, skill-gap analysis, mock interview and failover
KAN-6	Real-Time Communication	Chat, groups, presence, read receipts and notifications
KAN-7	Community & Events	Forum, events and alumni networking
KAN-8	Mobile Application	Android wrapper, mobile authentication, responsive UI and push
KAN-9	Security, Reliability & DevOps	Security hardening, failover, testing, CI/CD, monitoring
KAN-10	Scrum & Project Governance	Backlog, ceremonies, quality gates, risks, releases and metrics

7. User Stories and Acceptance Criteria

The Stories follow the user-story structure described in the supplied Scrum reference: As a <user>, I want to <perform an action>, so that <benefit>. In Alumnex Connect, the descriptions also include explicit Acceptance Criteria and a Suggested estimate. This combination supports backlog refinement, implementation and review.

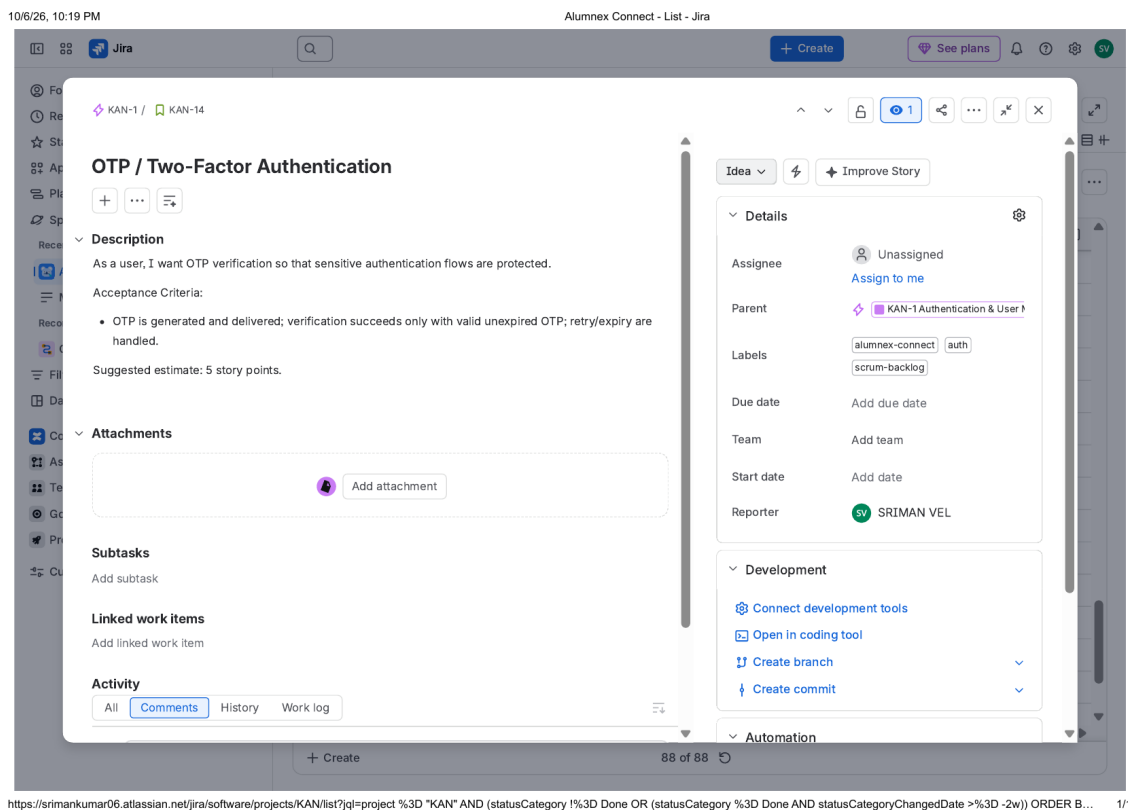


Figure 4. Jira Story detail example (KAN-14 OTP / Two-Factor Authentication) showing user story text, acceptance criteria, estimate, parent Epic and project labels.

For example, KAN-14 defines OTP behavior and explicitly states that valid, unexpired OTPs must succeed while retry and expiry handling must be supported. The Jira record also shows the parent Epic, labels, reporter and the suggested estimate. This is the level of detail expected for a refined backlog item.

8. Estimation and Story Points

All 53 Jira Stories contain a Suggested estimate value in the description. The distribution is 29 Stories at 5 points, 15 Stories at 3 points, 8 Stories at 8 points, and 1 Story at 2 points, giving a total of 256 suggested points. The supplied Story Point Baseline document explicitly states that these values are a planning baseline and not a claim of historical Sprint execution.

Alumnex Connect — Story Point Estimate Baseline

Alumnex Connect — Story Point Estimate Baseline

This page records the **Suggested estimate** values already embedded in the 53 Jira Story descriptions for project KAN. The estimates are a planning baseline, not a claim of historical Sprint execution.

Jira field constraint: the current KAN team-managed project does not expose a Story Points custom field in its issue-type metadata. The estimate values therefore remain documented in each story description and are consolidated here for reporting.

Baseline Summary

Metric	Value
Stories	53
Total suggested story points	256
Highest single estimate	8
Smallest estimate	2

Story-by-Story Register

Jira	Story	Epic	Phase	Points
KAN-11	Student Registration	Authentication & User Management	Phase 1 — Foundation	5
KAN-12	Student Login	Authentication & User Management	Phase 1 — Foundation	5
KAN-13	OAuth Authentication	Authentication & User Management	Phase 1 — Foundation	5

Figure 5. Story Point Estimate Baseline exported from Confluence/Jira documentation, showing the 53-story / 256-point baseline.

Jira configuration constraint: The KAN team-managed project does not expose a Story Points custom field in its issue-type metadata. The estimates are therefore retained in Story descriptions and in the baseline documentation instead of being represented as a nonexistent native field.

9. Board Workflow and Work-State Management

The board workflow is used as the project execution layer. Each state communicates where a work item is in its delivery lifecycle.

Board state	Operational meaning
Idea	Potential work or high-level capability not yet in execution
To Do	Refined work that is queued or awaiting execution
In Progress	Implementation actively underway
In Review	Testing, peer review or acceptance validation
Done	Work has passed the project quality/completion gate

9.1 Board population record

The board screenshot supplied at the beginning of the workflow showed 53 Story items in Idea, 5 Bugs in To Do, and zero board items in In Progress, In Review or Done. Subsequent Jira evidence shows the board populated across multiple workflow states. The current whole-project Jira Summary snapshot reports 88 total issues with 38 Done, 11 In Progress, 9 In Review, 20 To Do and 10 Idea; the 10 Idea issues are the Epic containers, while the board itself displays the 58 Story/Bug work items.

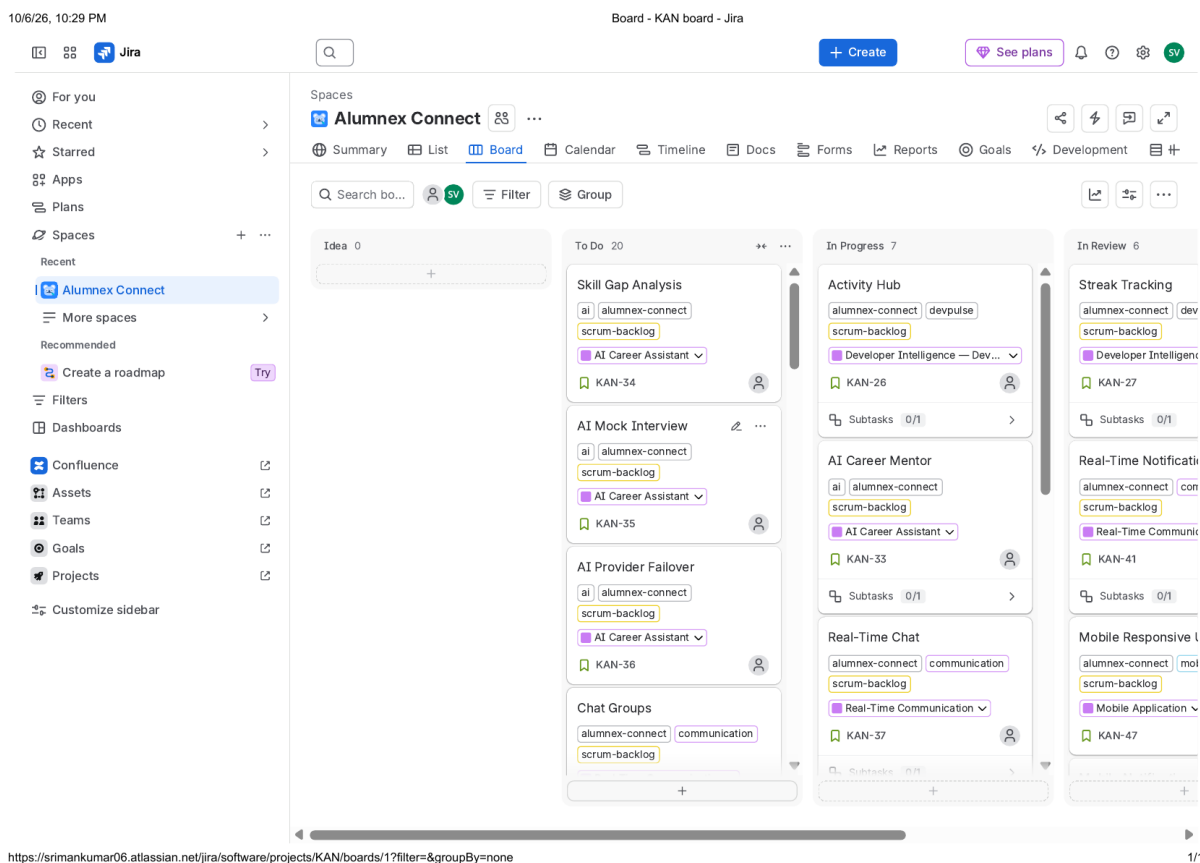


Figure 6. Jira Board evidence export after workflow population, showing To Do, In Progress and In Review work states; board work items are the executable Story/Bug layer.

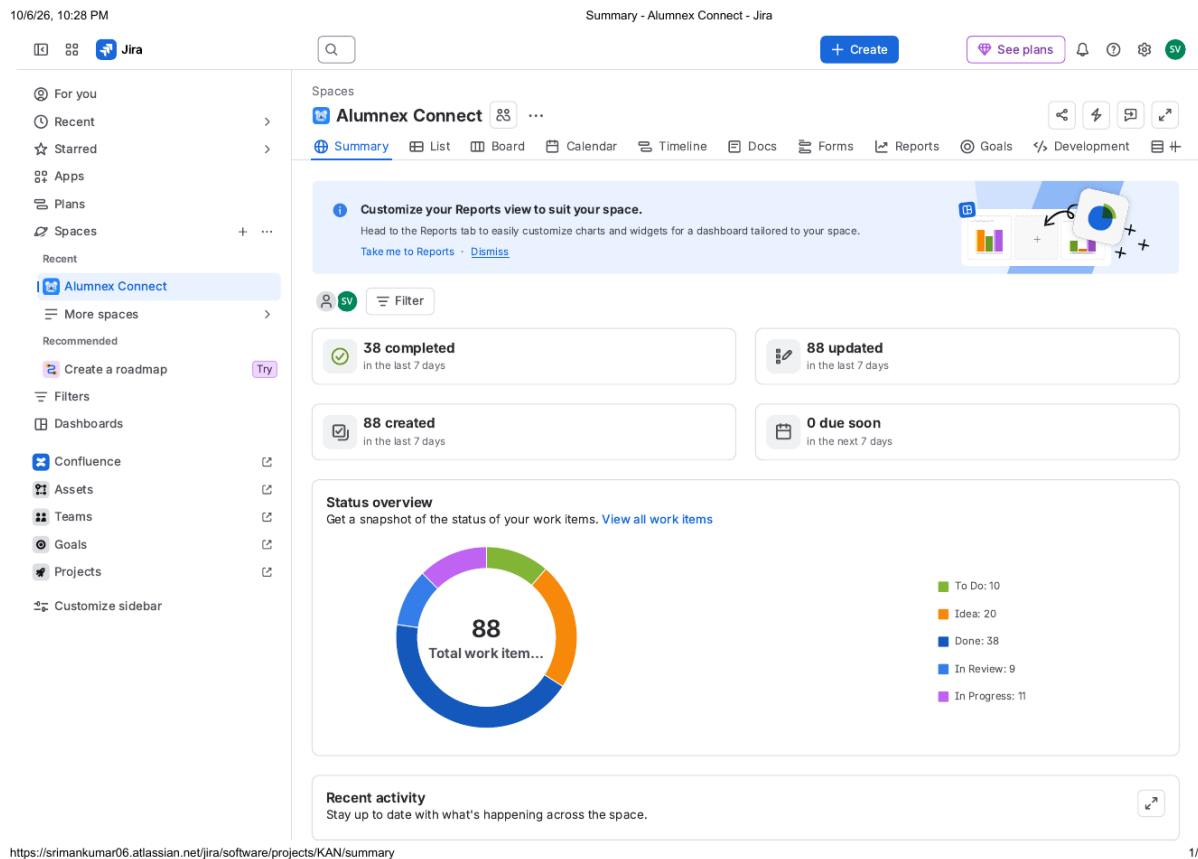


Figure 7. Jira Summary snapshot dated 06 October 2026 showing 88 total work items and the current distribution: 38 Done, 11 In Progress, 9 In Review, 20 To Do and 10 Idea.

Interpretation for an academic report: These status values are a current Jira management snapshot created to organize the project backlog and work-state view. They must not be presented as historical Sprint completion records.

10. Implementation Subtasks and Traceability

Twenty Subtasks were created so that implementation work can be connected to its parent Story. This is consistent with the practical Scrum reference, which recommends decomposing Stories into smaller technical tasks and then tracking their movement through the board.

Subtask	Work item	Parent Story
KAN-69	Design registration flow	KAN-11
KAN-70	Implement secure credential handling	KAN-11
KAN-71	Registration tests	KAN-11
KAN-72	Implement login flow	KAN-12
KAN-73	Handle authentication failures	KAN-12
KAN-74	Login tests	KAN-12
KAN-75	Mentor search and filters	KAN-17
KAN-76	Mentorship request workflow	KAN-18
KAN-77	Mentorship request tests	KAN-18
KAN-78	GitHub integration	KAN-22
KAN-79	Activity aggregation	KAN-26

KAN-80	Streak calculation	KAN-27
KAN-81	Resume PDF extraction	KAN-32
KAN-82	ATS scoring	KAN-32
KAN-83	AI chat integration	KAN-33
KAN-84	Socket messaging	KAN-37
KAN-85	Notification deduplication	KAN-41
KAN-86	Android wrapper	KAN-45
KAN-87	FCM registration	KAN-48
KAN-88	Security review	KAN-50

10/6/26, 10:18 PM Alumnex Connect - List - Jira

[+ Create](#) [See plans](#)    

Spaces

Alumnex Connect  ...

[Summary](#) [List](#) [Board](#) [Calendar](#) [Timeline](#) [Docs](#) [Forms](#) [Reports](#) [Goals](#) [Development](#) 

[Ask AI](#)  [Filter 2](#) [Group](#)  

☐	Work	Assignee	Reporter	Priority
☐	 KAN-10 Scrum & Project Governance	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-9 Security, Reliability & DevOps	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-8 Mobile Application	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-7 Community & Events	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-6 Real-Time Communication	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-5 AI Career Assistant	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-4 Career & Job Management	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-3 Developer Intelligence — DevPulse	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-2 Alumni-Student Mentorship	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-1 Authentication & User Management	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-68 Google Calendar Scope Access Denied	 Unassigned	 SRIMAN VEL	 Medium
☐	 KAN-66 Google OAuth Redirect URI Mismatch	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-65 FCM Push Notification Delivery Failure	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-64 Duplicate Reminder Notifications	 Unassigned	 SRIMAN VEL	 High
☐	 KAN-64 Daily Goal / Streak Synchronization Loss	 Unassigned	 SRIMAN VEL	 High

[+ Create](#) 88 of 88 

[https://srimankumar06.atlassian.net/jira/software/projects/KAN/list?ql=project %3D "KAN" AND %28statusCategory %21%3D Done OR %28statusCategory %3D Done AND statusCategoryChangedDate %3E%3D -2w%...](https://srimankumar06.atlassian.net/jira/software/projects/KAN/list?ql=project%3D%20KAN%20AND%20statusCategory%20%3D%20Done%20OR%20statusCategory%3D%20Done%20AND%20statusCategoryChangedDate%3E%3D%20-2w%20ago) 1/1

Figure 8. Jira List view showing implementation Subtasks and their traceable work items.

11. Release and Phase Management

Five Jira Versions were created to group work into coherent delivery phases. This creates a roadmap/release layer above the individual Story workflow.

Jira Version	Scope
Phase 1 - Foundation	Authentication, profiles, RBAC and platform foundation.
Phase 2 - Mentorship & Career	Mentorship workflows, jobs, applications and ATS.
Phase 3 - DevPulse	Developer integrations, activity hub and streak tracking.
Phase 4 - AI & Communication	AI career capabilities, chat and notifications.
Phase 5 - Mobile & Reliability	Mobile experience, security, failover, testing and monitoring.

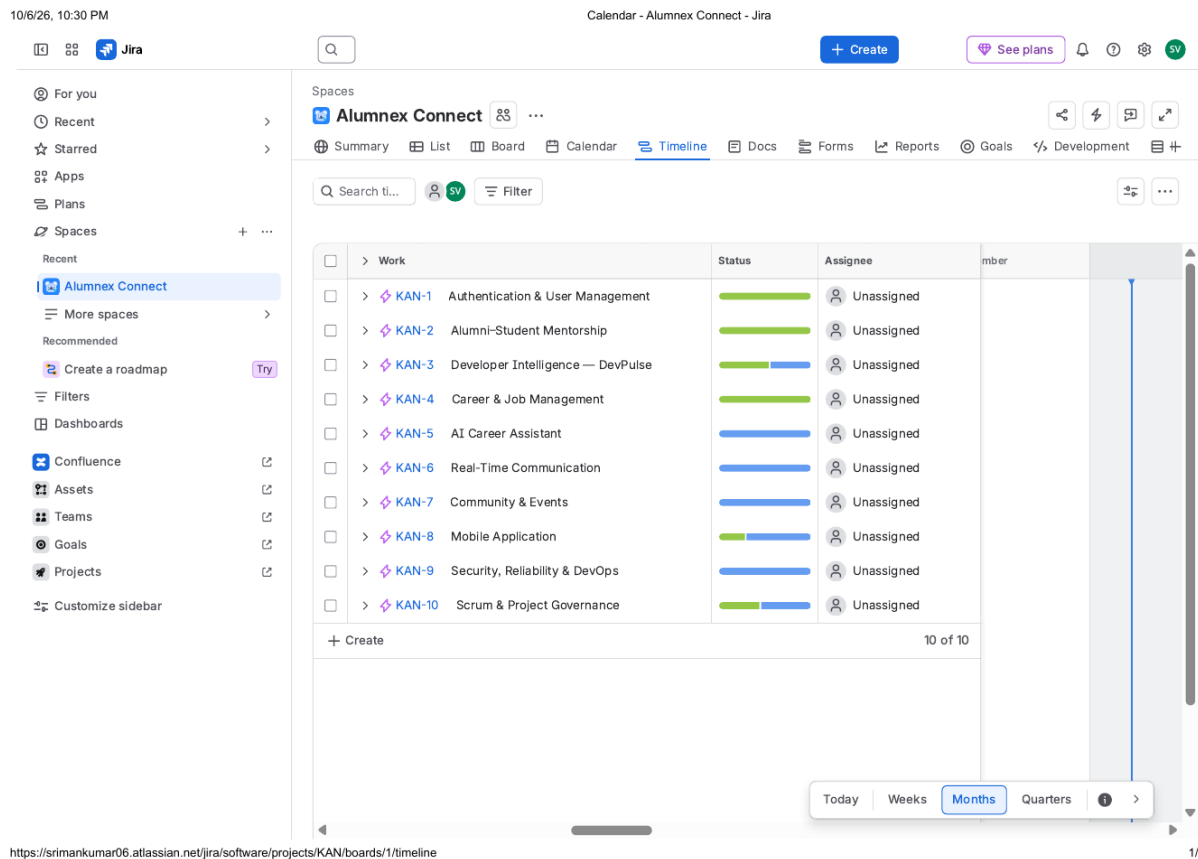


Figure 9. Jira Timeline view displaying the Epic-level product structure across the project roadmap.

In Agile terms, Versions are useful for release planning, while Sprints (when available) are time-boxed iteration contexts. The current KAN configuration provides the release-phase layer but not native Scrum Sprint execution.

12. Calendar and Scheduling View

The Calendar view provides a date-based perspective for work planning. The evidence export shows unscheduled work and makes it possible to assign due dates by dragging work items onto calendar dates. This supports scheduling and coordination, but does not by itself create a Sprint.

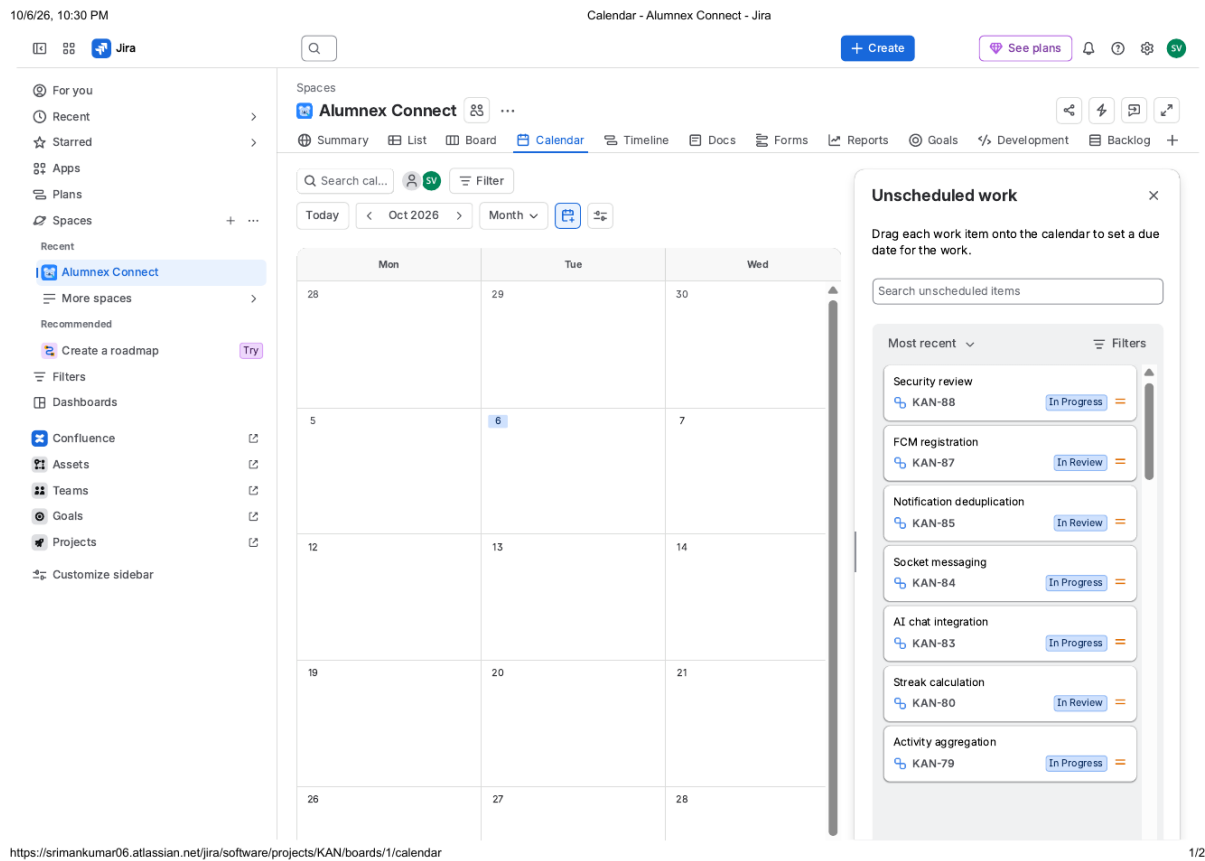


Figure 10. Jira Calendar view showing unscheduled work and work-state information.

13. Dependency Management

Eight issue links of type Blocks were created to make sequencing and risk visible. Dependency tracking is important because a technically valid Story may still be unable to progress until an upstream capability is available.

Source	Relationship	Target
KAN-33	blocks	KAN-36
KAN-45	blocks	KAN-46
KAN-48	blocks	KAN-66
KAN-26	blocks	KAN-64
KAN-41	blocks	KAN-65
KAN-13	blocks	KAN-67
KAN-33	blocks	KAN-68
KAN-50	blocks	KAN-52

Refinement note: During future backlog refinement, every Blocks relationship should be revalidated. If a relationship is informational rather than a hard sequencing constraint, a Relates link is more accurate than Blocks.

14. Defect Management

The project contains five observed/reported defects. Their descriptions include an observed problem statement, fix/acceptance criteria and a verification note. This is consistent with the supplied Scrum reference, which treats Bugs as visible work that progresses through an engineering lifecycle rather than being hidden outside the backlog.

Bug	Problem	Area	Fix / acceptance intent
KAN-64	Daily Goal / Streak Synchronization Loss	DevPulse	Persist goal completion, reconcile missed events, idempotent sync, expose last-sync timestamp.
KAN-65	Duplicate Reminder Notifications	Communication	Deduplicate by notification/event ID, coordinate delivery channels and add delivery logging.
KAN-66	FCM Push Notification Delivery Failure	Mobile	Validate FCM token lifecycle, credentials, retries and safe delivery logging.
KAN-67	Google OAuth Redirect URI Mismatch	Authentication	Align authorized redirect URIs with the active backend callback configuration.
KAN-68	Google Calendar Scope Access Denied	Career / Calendar	Review scopes and consent configuration, handle denial gracefully and document requirements.

All five Bugs are currently in To Do. They are explicitly marked in Jira as observed/reported defects and should be verified against the current implementation before being closed.

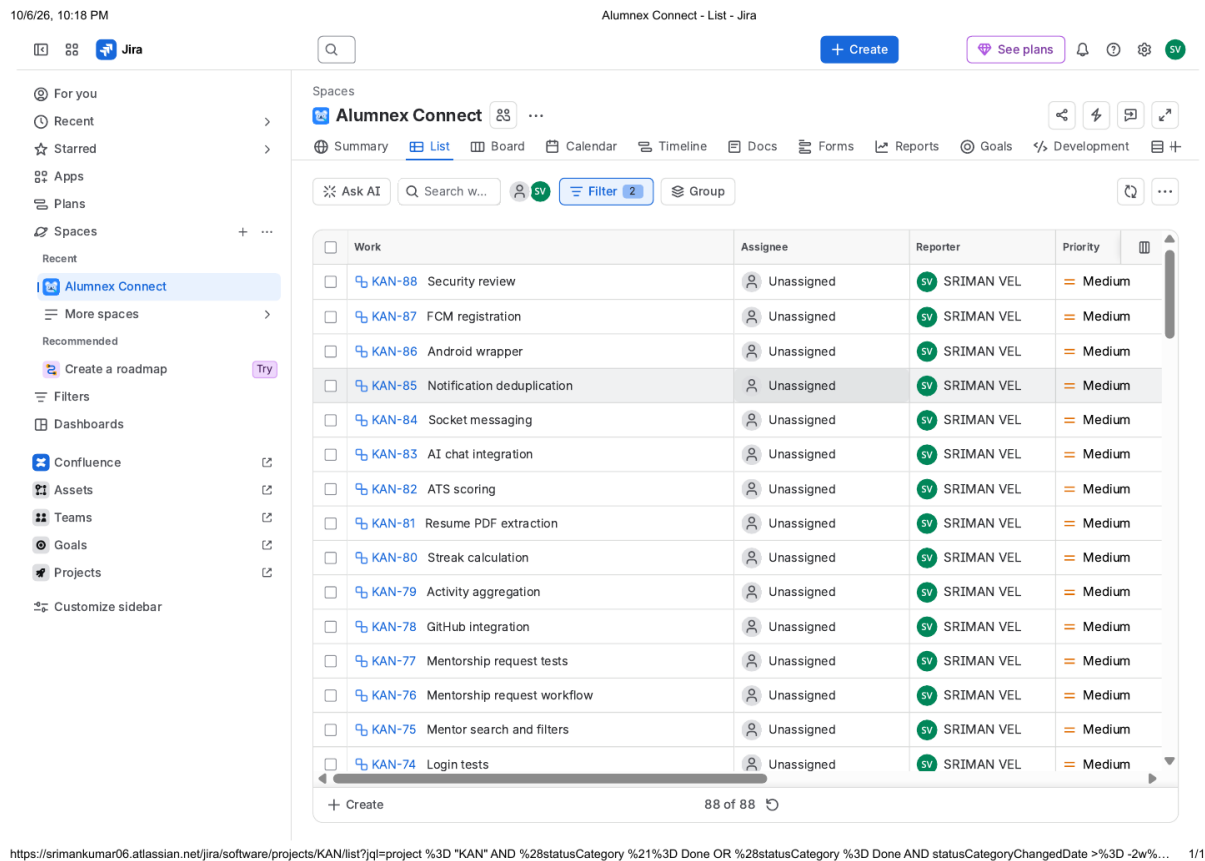


Figure 11. Jira List view showing the project work-item register, including Subtasks and reported Bugs.

15. Scrum Governance and Ceremonies

The governance layer is represented by KAN-55 through KAN-63 under the Scrum & Project Governance Epic. These issues define how a Scrum-style operating model would be run around the existing backlog.

Jira Story	Ceremony / governance practice	Application
KAN-55	Product Backlog & Refinement	Maintain clear outcomes, acceptance criteria and priorities.
KAN-56	Sprint Planning	Define Sprint Goal, selected work, estimates and capacity.
KAN-57	Daily Scrum Tracking	Inspect progress, blockers and plan adjustments.
KAN-58	Sprint Review & Stakeholder Feedback	Demonstrate increments and capture feedback.
KAN-59	Sprint Retrospective & Improvement Actions	Convert lessons into actionable improvements.
KAN-60	Definition of Ready & Definition of Done	Establish readiness and completion quality gates.
KAN-61	Risk, Dependency & Decision Tracking	Make important project constraints visible and traceable.
KAN-62	Release & Version Tracking	Connect backlog scope to delivery phases.
KAN-63	Agile Metrics & Continuous Improvement	Use delivery data for system improvement.

The practical Scrum reference also identifies roles such as Product Owner, Scrum Master, Developers and Tester. For Alumnex Connect, those roles are used as a process model; the connected Jira exports do not by themselves provide historical meeting attendance or role-assignment records, so this report does not invent such evidence.

15.1 Confluence documentation templates and where they fit

Template	Main content	Agile application
Project plan template	Driver, approver, contributors, objective, scope, timeline, milestones and status.	Project initiation, release planning and stakeholder alignment.
Meeting notes template	Date, participants, goals, discussion topics, action items, decisions and related information.	Daily Scrum, Sprint Planning, Review, Retrospective and stakeholder meetings.
Weekly status report template	Wins, needs input, focus, notes and important links.	Weekly stakeholder communication and management reporting.

16. Definition of Ready and Definition of Done

16.1 Definition of Ready (DoR)

- The user outcome is clear and valuable.
- Acceptance criteria are testable.
- Dependencies are known or explicitly tracked.
- Scope is small enough for the intended iteration.
- The team can explain what evidence will demonstrate success.

16.2 Definition of Done (DoD)

- Implementation is complete against the Story scope.
- Acceptance criteria are satisfied.
- Relevant automated/manual tests are completed.
- Code or implementation review is completed where applicable.
- Security/privacy considerations are addressed where relevant.
- Release/deployment requirements are satisfied when applicable.
- Required documentation is updated.

Agile application: DoR protects the quality of work entering execution; DoD protects the quality of work leaving execution. Together they create explicit quality gates rather than relying on a status label alone.

17. Jira Reporting, Metrics and Evidence

Jira provides Summary, Reports, Calendar, Timeline and Development views. The uploaded evidence demonstrates how the project can be reviewed from several angles rather than relying only on a board.

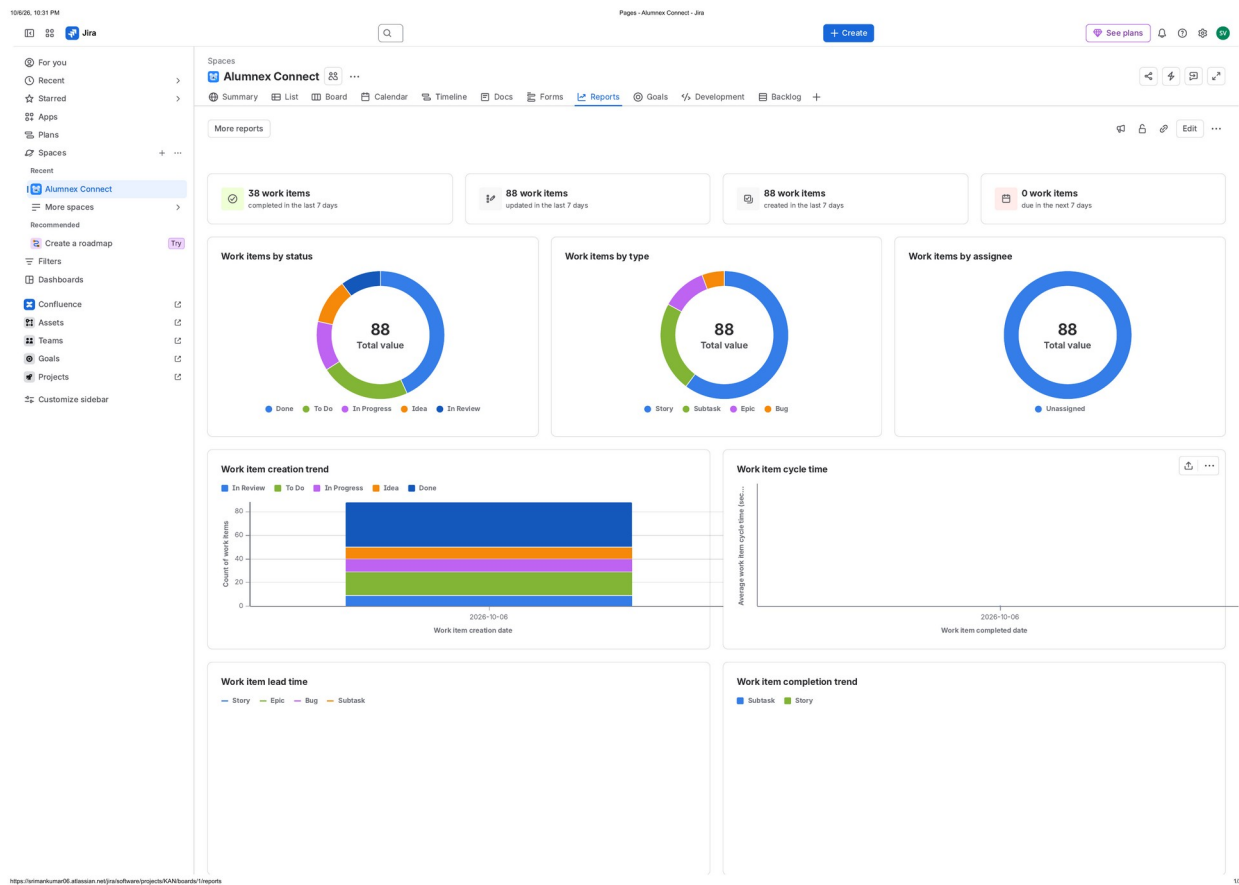


Figure 12. Jira Reports view showing work-item counts by status, type, assignee and trend-based views.

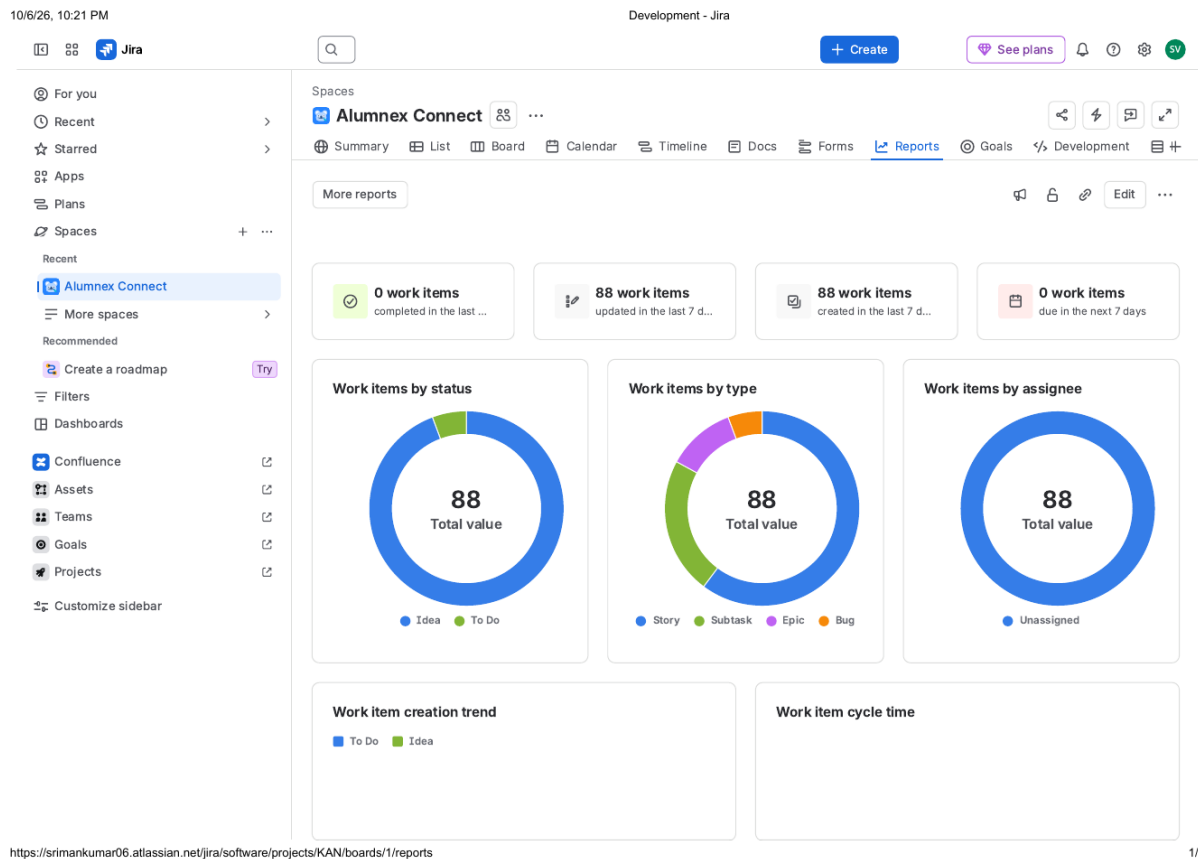


Figure 13. Jira Development view showing development connections and delivery metrics area.

The Reports evidence dated 06 October 2026 shows 38 work items completed in the last 7 days and 88 work items created/updated in that same period. Because the project-management structure was established in this period, these values primarily document Jira setup and state management rather than a historical product velocity.

Recommended Agile metrics for future real iterations are throughput, cycle time, work-item age, WIP, defect trends, release readiness and, after real Scrum Sprints exist, Sprint velocity and planned-versus-completed work.

18. Confluence Documentation and Knowledge Management

Confluence complements Jira by storing the narrative project-management layer. The dedicated Alumnex Connect Jira Project Management & Agile Playbook states that Jira is the source of truth for backlog, work status, defects, dependencies, releases and delivery metrics, while the playbook documents the Scrum model, backlog refinement, Sprint Planning, Daily Scrum, Sprint Review, Retrospective, DoR/DoD, risk/dependency tracking, release tracking and Agile metrics.

Alumnex Connect — Jira Project Management & Agile Playbook

Alumnex Connect Jira project-management and Agile/Scrum operating playbook.

Jira is the source of truth for backlog, work status, defects, dependencies, releases and delivery metrics.

Scrum model

- Product Backlog and refinement
- Sprint Planning
- Daily Scrum
- Sprint Review
- Sprint Retrospective
- Definition of Ready / Definition of Done
- Risk, dependency and decision tracking
- Release and version tracking
- Agile metrics and continuous improvement

Product areas

Authentication & User Management; Alumni–Student Mentorship; Developer Intelligence — DevPulse; Career & Job Management; AI Career Assistant; Real-Time Communication; Community & Events; Mobile Application; Security, Reliability & DevOps; Scrum & Project Governance.

Defect lifecycle

Record reproducible defects with observed behavior, expected behavior, impact, acceptance/fix criteria and verification notes. Do not close without validation.

Important configuration note

The current KAN board is a simple/team-managed board and does not support Jira Scrum sprints. Therefore no historical or active sprint records are being fabricated. The Scrum backlog and governance model are represented in Jira now; a Scrum-capable board can later use the same backlog for real Jira Sprints.

Reconstruction note

Because Alumnex Connect is already developed and the Jira project previously contained no issues, the created backlog and governance artifacts are a structured

Figure 14. Confluence Agile/Scrum playbook used as the project-management documentation layer.

19. How Agile Methodologies Apply to Alumnex Connect

Artifact / practice	Methodology	Jira evidence	Why it matters
Product Backlog	Scrum	KAN-11 to KAN-63 plus Bugs and Subtasks	Defines and prioritizes the work that can deliver product

			value.
Epic hierarchy	Scrum / Agile	KAN-1 to KAN-10	Groups large capability areas into manageable product outcomes.
User Stories	Scrum / Agile	53 Stories	Express work from the user perspective and create vertical increments.
Acceptance Criteria	Scrum / quality	Story descriptions	Create observable completion conditions for testing and review.
Subtasks	Agile / engineering	KAN-69 to KAN-88	Break implementation into smaller technical activities.
Workflow board	Kanban	KAN board	Makes flow, WIP and review stages visible.
Story estimates	Scrum / planning	Suggested estimates in 53 Stories	Support relative sizing; future Sprints can use them after native point support exists.
Bugs	Agile quality	KAN-64 to KAN-68	Treat defects as visible work with fix criteria and verification.
Versions	Release planning	Five Phase Versions	Organize delivery scope by release/phase.
Dependencies	Lean / Scrum planning	8 Blocks links	Surface sequencing risk and prevent hidden blockers.
DoR / DoD	Scrum	KAN-60	Control readiness and completion quality.
Retrospective	Scrum / continuous improvement	KAN-59	Convert experience into process improvements.
Automated testing / CI-CD	XP	KAN-52 / KAN-53	Reduce regression risk and shorten feedback loops.
Metrics	Kanban / Lean / Scrum	KAN-63 + Jira Reports	Use evidence to improve flow and planning.

20. Project Execution Record

The following sequence records the Jira-based project-management actions represented in the current workspace. It is intended as an auditable management log, not as a claim that every action occurred historically on the same date as the original software-development work.

Step	Execution record
1	Project structure established: Alumnex Connect / KAN project and KAN board verified.
2	Epic layer created: 10 product capability Epics created to organize the solution.
3	Story backlog built: 53 user Stories created with user-oriented descriptions and acceptance criteria.
4	Implementation decomposition: 20 Subtasks created for selected Stories.
5	Defect visibility: 5 observed/reported Bugs created with fix/acceptance criteria.
6	Release grouping: 5 Jira Versions created and non-Epic work assigned to the relevant phase.
7	Dependencies: 8 Blocks relationships recorded between related work items.
8	Workflow population: Stories/Subtasks were distributed across To Do, In Progress, In Review and Done to create a meaningful current work-state view.
9	Estimation baseline: 53 suggested Story estimates

	consolidated into a 256-point planning baseline.
10	Governance documentation: KAN-55 to KAN-63 and the Confluence Agile/Scrum playbook established the operating model.
11	Evidence capture: Backlog, Board, Summary, Calendar, Timeline, Reports, Development and Story-detail views exported for evidence.
12	Academic documentation: This report consolidates the project-management record and explains the Agile methodology mapping.

20.1 Current project status snapshot

Measure	Current value	Interpretation
Whole Jira project	88 issues	10 Epics, 53 Stories, 20 Subtasks, 5 Bugs
Whole-project status	38 Done / 11 In Progress / 9 In Review / 20 To Do / 10 Idea	Includes Epics and Subtasks
Board work-item layer	58 displayed Stories/Bugs	25 Done / 7 In Progress / 6 In Review / 20 To Do / 0 Idea
Release phases	5	Phase 1 to Phase 5
Suggested Story Points	256	53 Stories

21. Challenges, Constraints and Academic Reporting Rules

Constraint	Academic treatment
No native Scrum Sprint history	The KAN board is simple/team-managed and does not support native Jira Scrum Sprints. Therefore this report documents Scrum practices as an operating model, not as historical Sprint evidence.
No native Story Points field	The project metadata exposes no Story Points custom field. The 256-point baseline is retained in Story descriptions and documentation.
Observed Bugs require verification	The five Bugs are recorded from observed/reported behavior and should be re-tested against the current implementation before closure.
Dependency semantics	The eight Blocks links should be revalidated during future refinement to ensure that each is truly a blocker.
Assignment evidence	The exported issue views show many items as Unassigned; this report does not invent individual responsibility assignments.
Jira metrics timing	The 06 October 2026 reports show recent creation/update activity because the project-management structure was established recently.

22. Results and Outcomes

- Created a structured Agile backlog with 10 Epics, 53 Stories, 20 Subtasks and 5 Bugs.
- Organized the product into five release/phase Versions.
- Established a visible flow-based Jira board with five workflow states.
- Created traceability between Stories and implementation Subtasks.
- Recorded observed defects with acceptance/fix criteria and verification notes.
- Established dependency visibility through issue links.
- Created a documented estimation baseline of 256 suggested Story Points.

- Added Scrum governance artifacts covering backlog refinement, planning, Daily Scrum, Review, Retrospective, DoR/DoD, risks, releases and metrics.
- Built a Confluence knowledge layer and captured Jira/Confluence UI evidence for the academic report.

23. Conclusion

The Alumnex Connect Jira workspace now provides a structured Agile project-management record connecting product capabilities, user requirements, implementation work, quality issues, release phases, dependencies and governance. The board provides a clear flow-based work view, while Confluence provides the supporting process documentation.

The strongest current methodological fit is a hybrid Agile model: Scrum governs how the backlog should be refined, planned, reviewed and improved; Kanban provides the actual visible workflow in the current team-managed Jira board; XP principles can strengthen engineering quality through automated testing and CI/CD; and Lean principles support waste reduction, short feedback loops and flow improvement.

For a future iteration in which native Scrum reporting is required, the project should be migrated or recreated in a Scrum-capable Jira configuration and the same backlog, acceptance criteria, Subtasks, Bugs and release structure can then be used to manage real time-boxed Sprints.

Appendix A - Complete Epic Register

KAN-1 - Authentication & User Management

Identity, registration, login, OAuth, OTP, profiles, RBAC

KAN-2 - Alumni-Student Mentorship

Mentor discovery, requests, sessions, reviews

KAN-3 - Developer Intelligence - DevPulse

Coding-platform integrations, activity hub and streaks

KAN-4 - Career & Job Management

Job posting, browsing, applications and ATS

KAN-5 - AI Career Assistant

AI mentor, skill-gap analysis, mock interview and failover

KAN-6 - Real-Time Communication

Chat, groups, presence, read receipts and notifications

KAN-7 - Community & Events

Forum, events and alumni networking

KAN-8 - Mobile Application

Android wrapper, mobile authentication, responsive UI and push

KAN-9 - Security, Reliability & DevOps

Security hardening, failover, testing, CI/CD, monitoring

KAN-10 - Scrum & Project Governance

Backlog, ceremonies, quality gates, risks, releases and metrics

Appendix B - Story Register

Jira	Story	Epic	Current status	Suggested points
KAN-11	Student Registration	KAN-1	Done	5
KAN-12	Student Login	KAN-1	Done	5
KAN-13	OAuth Authentication	KAN-1	Done	5
KAN-14	OTP / Two-Factor Authentication	KAN-1	Done	5
KAN-15	User Profile Management	KAN-1	Done	3
KAN-16	Role-Based Access Control	KAN-1	Done	5
KAN-17	Browse Alumni Mentors	KAN-2	Done	5
KAN-18	Request Mentorship	KAN-2	Done	5
KAN-19	Manage Mentorship Requests	KAN-2	Done	5
KAN-20	Mentorship Session	KAN-2	Done	5

	Tracking			
KAN-21	Mentorship Reviews	KAN-2	Done	3
KAN-22	GitHub Developer Statistics	KAN-3	Done	5
KAN-23	LeetCode Statistics	KAN-3	Done	5
KAN-24	Codeforces Statistics	KAN-3	Done	5
KAN-25	Unified Developer Profile	KAN-3	Done	3
KAN-26	Activity Hub	KAN-3	In Progress	8
KAN-27	Streak Tracking	KAN-3	In Review	5
KAN-28	Job Posting	KAN-4	Done	5
KAN-29	Browse Job Opportunities	KAN-4	Done	5
KAN-30	Apply for Jobs	KAN-4	Done	5
KAN-31	Job Application Management	KAN-4	Done	5
KAN-32	ATS Resume Analysis	KAN-4	Done	8
KAN-33	AI Career Mentor	KAN-5	In Progress	8
KAN-34	Skill Gap Analysis	KAN-5	To Do	8
KAN-35	AI Mock Interview	KAN-5	To Do	8
KAN-36	AI Provider Failover	KAN-5	To Do	5
KAN-37	Real-Time Chat	KAN-6	In Progress	8
KAN-38	Chat Groups	KAN-6	To Do	5
KAN-39	Online Presence	KAN-6	To Do	3
KAN-40	Read Receipts	KAN-6	To Do	3
KAN-41	Real-Time Notifications	KAN-6	In Review	5
KAN-42	Community Forum	KAN-7	To Do	5
KAN-43	Event Management	KAN-7	To Do	5
KAN-44	Alumni Networking	KAN-7	To Do	5
KAN-45	Android Mobile Wrapper	KAN-8	Done	8
KAN-46	Mobile Authentication	KAN-8	In Progress	5
KAN-47	Mobile Responsive UI	KAN-8	In Review	5
KAN-48	Mobile Notifications	KAN-8	In Review	5
KAN-49	Android APK Build & Release	KAN-8	To Do	3
KAN-50	Security Hardening	KAN-9	In Progress	8
KAN-51	API Failover	KAN-9	To Do	5
KAN-52	Automated Testing	KAN-9	In Review	5
KAN-53	CI/CD Pipeline	KAN-9	To Do	5
KAN-54	Production Monitoring	KAN-9	To Do	3
KAN-55	Product Backlog & Refinement	KAN-10	Done	3
KAN-56	Sprint Planning	KAN-10	Done	3
KAN-57	Daily Scrum Tracking	KAN-10	In Progress	2
KAN-58	Sprint Review & Stakeholder Feedback	KAN-10	To Do	3
KAN-59	Sprint Retrospective & Improvement Actions	KAN-10	To Do	3
KAN-60	Definition of Ready & Definition of Done	KAN-10	Done	3
KAN-61	Risk, Dependency & Decision Tracking	KAN-10	In Progress	3
KAN-62	Release & Version Tracking	KAN-10	Done	3
KAN-63	Agile Metrics & Continuous Improvement	KAN-10	In Review	3

Appendix C - Subtask Register

Jira	Subtask	Parent Story	Current status
KAN-69	Design registration flow	KAN-11	Done
KAN-70	Implement secure credential handling	KAN-11	Done
KAN-71	Registration tests	KAN-11	Done
KAN-72	Implement login flow	KAN-12	Done
KAN-73	Handle authentication failures	KAN-12	Done
KAN-74	Login tests	KAN-12	Done
KAN-75	Mentor search and filters	KAN-17	Done
KAN-76	Mentorship request workflow	KAN-18	Done
KAN-77	Mentorship request tests	KAN-18	Done
KAN-78	GitHub integration	KAN-22	Done
KAN-79	Activity aggregation	KAN-26	In Progress
KAN-80	Streak calculation	KAN-27	In Review
KAN-81	Resume PDF extraction	KAN-32	Done
KAN-82	ATS scoring	KAN-32	Done
KAN-83	AI chat integration	KAN-33	In Progress
KAN-84	Socket messaging	KAN-37	In Progress
KAN-85	Notification deduplication	KAN-41	In Review
KAN-86	Android wrapper	KAN-45	Done
KAN-87	FCM registration	KAN-48	In Review
KAN-88	Security review	KAN-50	In Progress

Appendix D - Bug Register

Bug	Summary	Area	Current status	Priority
KAN-64	Daily Goal / Streak Synchronization Loss	DevPulse	To Do	High
KAN-65	Duplicate Reminder Notifications	Communication	To Do	High
KAN-66	FCM Push Notification Delivery Failure	Mobile	To Do	High
KAN-67	Google OAuth Redirect URI Mismatch	Authentication	To Do	High
KAN-68	Google Calendar Scope Access Denied	Career / Calendar	To Do	Medium

Appendix E - Screenshot Evidence Log

Figure	Screen	Evidence source	What it proves
Figure 1	Jira Backlog - page 1	Alumnex Connect - Backlog - Jira.pdf	Evidence of backlog structure and Epic/Story grouping.
Figure 2	Jira Backlog - page 2	Alumnex Connect - Backlog - Jira.pdf	Continued Story register.
Figure 3	Jira Board before workflow population	User-provided screenshot	Initial state: 53 Stories in Idea, 5 Bugs in To Do.
Figure 4	Jira Story detail	Alumnex Connect - 2FA- Jira.pdf	Story structure, Acceptance Criteria, estimate, parent Epic and labels.
Figure 5	Story Point baseline	MFS-Alumnex Connect - Story Point Estimate Baseline PDF	53 Stories and 256 suggested points.
Figure 6	Jira Board workflow	Board - KAN board - Jira.pdf	Visible To Do, In Progress and In Review flow states.
Figure 7	Jira Summary	Summary - Alumnex Connect - Jira.pdf	88 total work items and current status distribution.
Figure 8	Jira List / implementation register	Alumnex Connect - List2 - Jira.pdf	Subtasks and implementation work.
Figure 9	Jira Timeline	Timeline - Alumnex Connect - Jira.pdf	Epic-level roadmap view.
Figure 10	Jira Calendar	Calendar - Alumnex Connect - Jira.pdf	Date-based planning and unscheduled work.
Figure 11	Jira List	Alumnex Connect - List - Jira.pdf	Project issue register and visible tracking.
Figure 12	Jira Reports	Pages - Alumnex Connect - Jira.pdf	Status, work type, creation and completion reporting.
Figure 13	Jira Development	Development - Jira.pdf	Development connections and technical delivery metrics area.
Figure 14	Confluence Agile/Scrum playbook	MFS-Alumnex Connect - Jira Project Management & Agile Playbook PDF	Process, governance, quality and Agile documentation.

References

- 1. Practical Scrum Process Using Jira (uploaded reference document).** Used as the methodology/process reference for requirements, Stories, Epics, estimation, Sprint planning, task decomposition, Daily Scrum, testing, Bugs, Review, Retrospective and reporting.
- 2. Alumnex Connect - Jira Project Management & Agile Playbook (Confluence export).** Used as the project-specific governance source for Scrum model, quality gates, dependency management, releases and reporting.
- 3. Alumnex Connect - Story Point Estimate Baseline (Confluence export).** Used for the 53-story / 256-point planning baseline and the Story Points field constraint.
- 4. Alumnex Connect Jira UI exports: Backlog, Board, Summary, List, List2, Calendar, Timeline, Reports/Pages, Development and Story detail.** Used as direct visual evidence of the Jira workspace and its project-management configuration on 06 October 2026.
- 5. Confluence templates: Project plan, Meeting notes and Weekly status report.** Used to explain how project plans, meeting records and weekly reporting fit into Agile governance and stakeholder communication.

srimankumar06

Overview

Directory

Users

Groups

Teams

Managed accounts

Service accounts

Domains

Apps

Rovo

Connectors

Security

Data management

Insights

Billing

Organization settings

Users

SRIMAN VEL

Organization admin

Grant access

Add to group

...



External user

srimankumar06@gmail.com

Details managed by the user

Active
Last seen September 12, 2026

Apps Groups Site admin

Search by app name

App

Showing results

App	Last seen	Plan	Roles	Actions
 Assets srimankumar06	 Failed to load	Free	App admin ×	...
 Confluence srimankumar06	 Failed to load	Premium	App admin × User :	...
 Goals srimankumar06	 Failed to load	Free	App admin ×	...
 Jira Administration srimankumar06	 Failed to load	None	App admin ×	...
 Jira srimankumar06	 Failed to load	Premium	User ×	...
 Projects srimankumar06	 Failed to load	Free	App admin ×	...
 Studio Studio	 Failed to load	Free	App admin ×	...

For you

Teams

People

Kudos

Goals

Projects

People



SRIMAN VEL

+ Add role details

Account settings

[Overview](#) Goals Projects Kudos

Working with me

e.g. I prefer async updates in Confluence. For urgent questions, ping me between 9am–3pm.

Recent work ⓘ

- Alumnex Connect — Current Jira Board Status Snapshot**
Confluence Page • My first space 8 minutes ago
- Alumnex Connect — Complete Agile & Jira Documentation**
Confluence Page • My first space 22 minutes ago
- Scrum & Project Governance**
Jira Comment • Alumnex Connect 48 minutes ago
- Alumnex Connect — Story Point Estimate Baseline**
Confluence Page • My first space 48 minutes ago
- Security review**
Jira Issue • Alumnex Connect 1 hour ago
- FCM registration**
Jira Issue • Alumnex Connect 1 hour ago

Show more

Reporting line

Details

Email **srimankumar06@gmail.com**

Teams




See all the teams you're a part of

Bring your collaborators together with teams you can @mention, filter, and assign work to.
[What are teams?](#)

+ Create team Browse teams

Frequent spaces

Alumnex Connect
Jira space



See manager and direct reports

Add manager information in your identity provider, and show a tree of manager and direct reports on profiles

- ## Spaces

 Alumnex Connect






- [Summary](#)
[List](#)
[Board](#)
[Calendar](#)
[Timeline](#)
[Docs](#)
[Forms](#)
[Reports](#)
[Goals](#)
[Development](#)
[Backlog](#)
[+](#)

🔍 Search backlog















Filter




☐ **Board** (58 work items)

53 5 0

☒	KAN-11	Student Registration	🔖	Authentication & U...	Idea ▾	👤
☒	KAN-12	Student Login	🔖	Authentication & U...	Idea ▾	👤
☒	KAN-13	OAuth Authentication		Authentication & U...	Idea ▾	👤
☒	KAN-14	OTP / Two-Factor Authentication		Authentication & U...	Idea ▾	👤
☒	KAN-15	User Profile Management		Authentication & U...	Idea ▾	👤
☒	KAN-16	Role-Based Access Control		Authentication & U...	Idea ▾	👤
☒	KAN-17	Browse Alumni Mentors	🔖	Alumni-Student M...	Idea ▾	👤
☐	KAN-18	Request Mentorship	🔖	Alumni-Student M...	Idea ▾	👤
☒	KAN-19	Manage Mentorship Requests		Alumni-Student M...	Idea ▾	👤
☒	KAN-20	Mentorship Session Tracking		Alumni-Student M...	Idea ▾	👤
☒	KAN-21	Mentorship Reviews		Alumni-Student M...	Idea ▾	👤
☒	KAN-22	GitHub Developer Statistics	🔖	Developer Intellige...	Idea ▾	👤
☒	KAN-23	LeetCode Statistics		Developer Intellige...	Idea ▾	👤
☒	KAN-24	Codeforces Statistics		Developer Intellige...	Idea ▾	👤
☒	KAN-25	Unified Developer Profile		Developer Intellige...	Idea ▾	👤
☒	KAN-26	Activity Hub	🔖	Developer Intellige...	Idea ▾	👤
☒	KAN-27	Streak Tracking	🔖	Developer Intellige...	Idea ▾	👤
☒	KAN-28	Job Posting		Career & Job Man...	Idea ▾	👤
☒	KAN-29	Browse Job Opportunities		Career & Job Man...	Idea ▾	👤

 KAN-30	Apply for Jobs		 Career & Job Man...	 Idea ▾	
 KAN-31	Job Application Management		 Career & Job Man...	 Idea ▾	
 KAN-32	ATS Resume Analysis		 Career & Job Man...	 Idea ▾	
 KAN-33	AI Career Mentor		 AI Career Assistant	 Idea ▾	
 KAN-34	Skill Gap Analysis		 AI Career Assistant	 Idea ▾	
 KAN-35	AI Mock Interview		 AI Career Assistant	 Idea ▾	
 KAN-36	AI Provider Failover		 AI Career Assistant	 Idea ▾	
 KAN-37	Real-Time Chat		 Real-Time Commu...	 Idea ▾	
 KAN-38	Chat Groups		 Real-Time Commu...	 Idea ▾	
 KAN-39	Online Presence		 Real-Time Commu...	 Idea ▾	
 KAN-40	Read Receipts		 Real-Time Commu...	 Idea ▾	
 KAN-41	Real-Time Notifications		 Real-Time Commu...	 Idea ▾	

+ Create



58 of 58 work items visible

▼

Backlog

(0 work items)

000

Your backlog is empty.

+ Create



Install Claude Agent for Jira

- [Rovo agents](#)
- [Link GitHub workflows to Jira](#)
- [Integrate Jira with development tools](#)
- [Security feature Jira](#)

Security tools

Connect security tools to monitor vulnerabilities in your codebase.






Install GitHub Security



Install Snyk Security in Jira Cloud



How was your experience with the Development page? [Give us feedback](#)

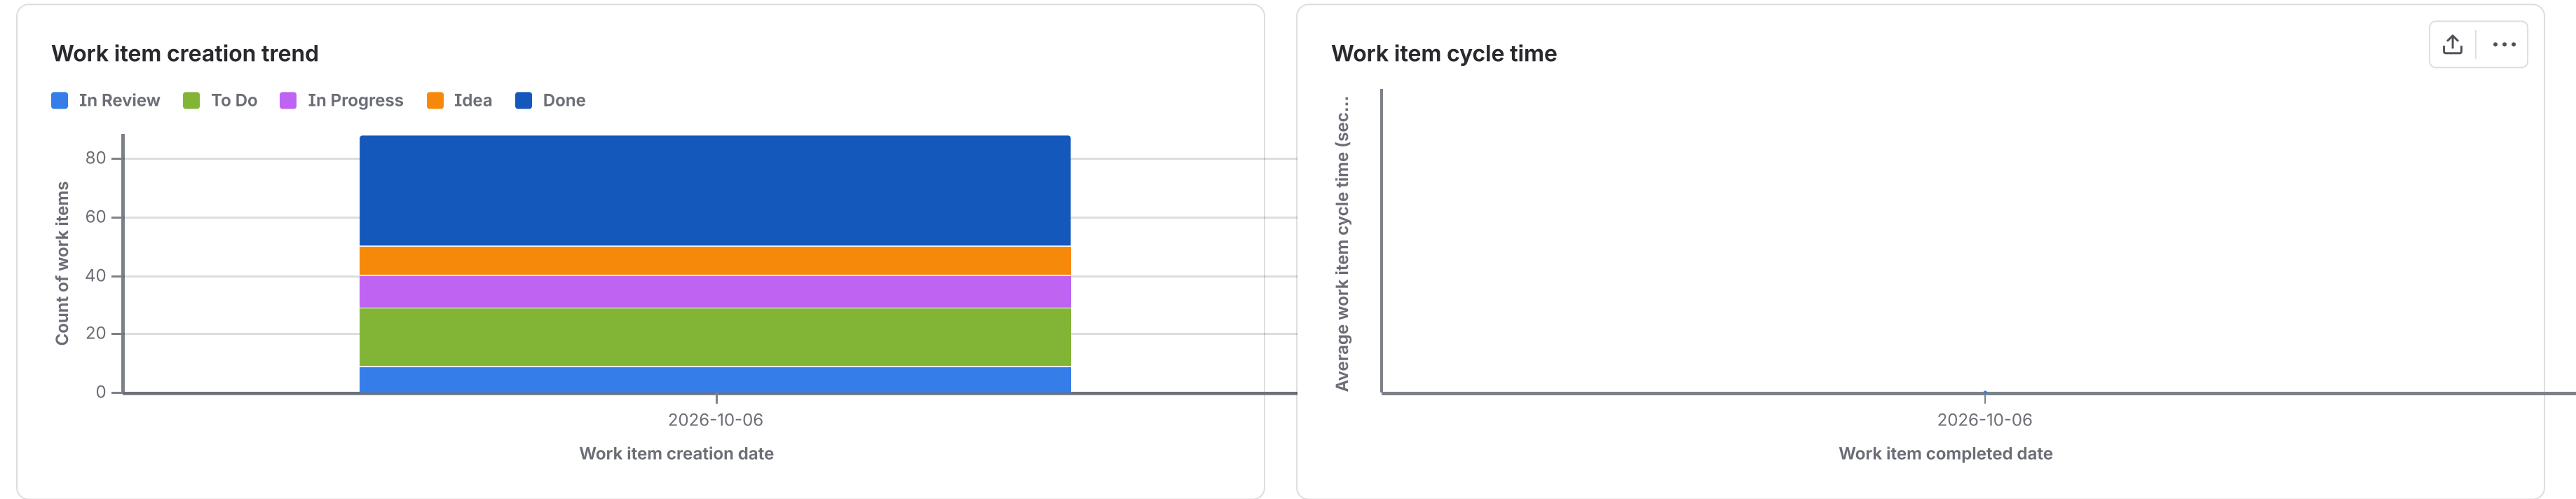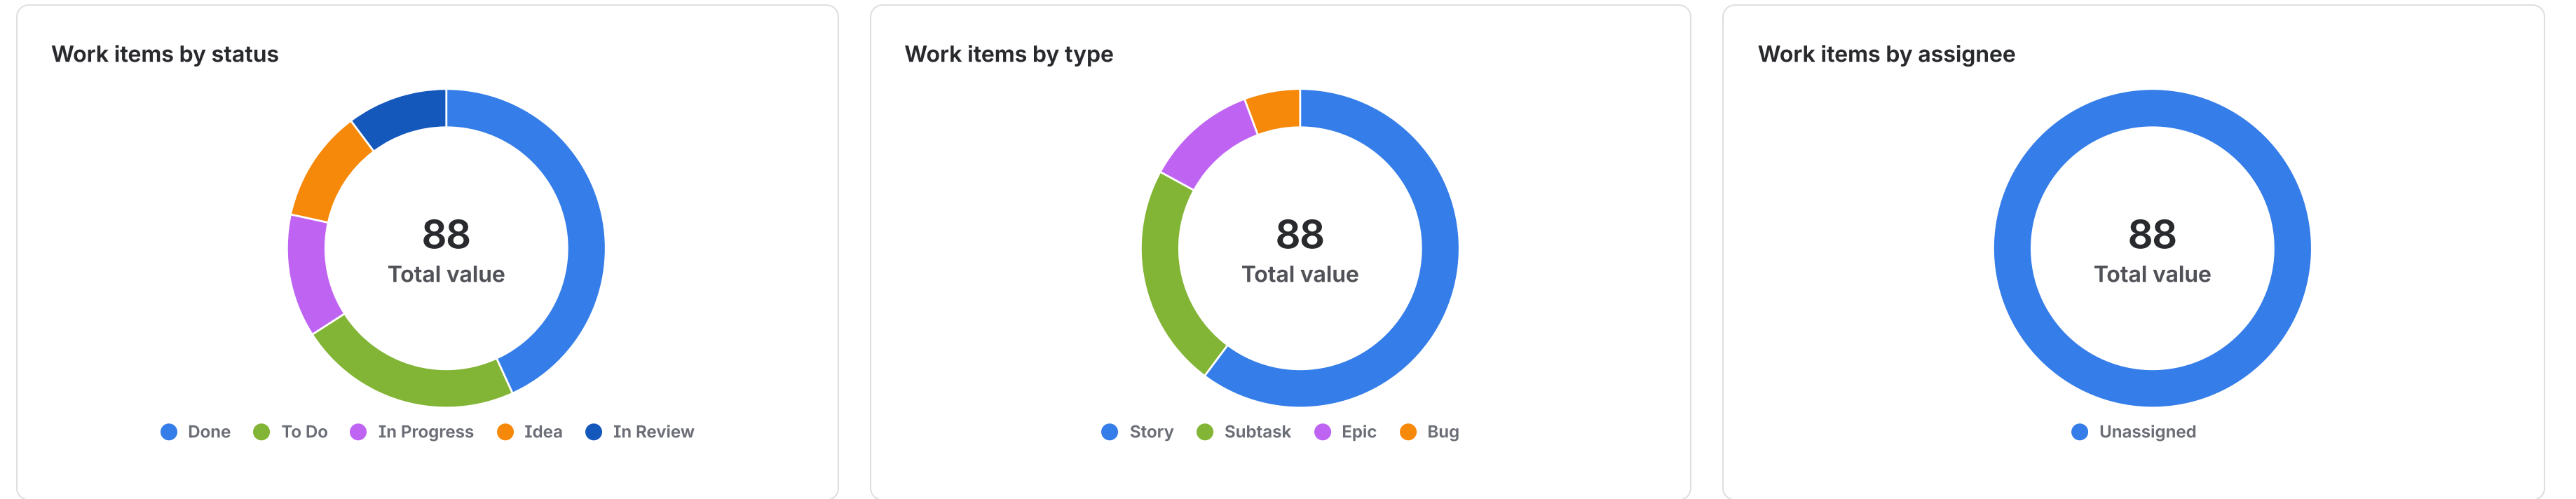

cycle time (seconds)

work items

Work item details

Q Search table

Work item key ▾	Work type ▾	Work item priority ▾	Issue summary ▾
KAN-1	⚡ Epic	⬇ High	Authentication & User Management
KAN-10	⚡ Epic	⬇ High	Scrum & Project Governance
KAN-11	🔖 Story		Student Registration
KAN-12	🔖 Story	⬆ Highest	Student Login
KAN-13	🔖 Story	⬇ High	OAuth Authentication
KAN-14	🔖 Story	⬇ High	OTP / Two-Factor Authentication
KAN-15	🔖 Story	⬇ High	User Profile Management
KAN-16	🔖 Story	⬇ High	Role-Based Access Control
KAN-17	🔖 Story	⬆ Highest	Browse Alumni Mentors

< 1 2 3 4 5 >

Showing rows 1-20 of 88

- ## Spaces

[Summary](#)
[List](#)
[Board](#)
[Calendar](#)
[Timeline](#)
[Docs](#)
[Forms](#)
[Reports](#)
[Goals](#)
[Development](#)

Q Search ti...



Filter

...

☐	> Work	Status	Assignee	Member
☐	> ⚡ KAN-1 Authentication & User Management		 Unassigned	
☐	> ⚡ KAN-2 Alumni-Student Mentorship		 Unassigned	
☐	> ⚡ KAN-3 Developer Intelligence — DevPulse		 Unassigned	
☐	> ⚡ KAN-4 Career & Job Management		 Unassigned	
☐	> ⚡ KAN-5 AI Career Assistant		 Unassigned	
☐	> ⚡ KAN-6 Real-Time Communication		 Unassigned	
☐	> ⚡ KAN-7 Community & Events		 Unassigned	
☐	> ⚡ KAN-8 Mobile Application		 Unassigned	
☐	> ⚡ KAN-9 Security, Reliability & DevOps		 Unassigned	
☐	> ⚡ KAN-10 Scrum & Project Governance		 Unassigned	

+ Create

10 of 10

Today | Weeks | **Months** | Quarters |  >

- In Progress =

Mon	Tue	Wed

Google OAuth Redirect URI Mismatch

 KAN-67

To Do ^

- For you
- Recent
- Starred
- Apps
- Plans
- Spaces
 - Recent
 - Alumnex Connect
 - More spaces
- Recommended
 - Create a roadmap
- Filters
- Dashboards
- Confluence
- Assets
- Teams
- Goals
- Projects
- Customize sidebar

Spaces

Alumnex Connect

- Summary
- List
- Board
- Calendar
- Timeline
- Docs
- Forms
- Reports
- Goals
- Development

Customize your Reports view to suit your space.
Head to the Reports tab to easily customize charts and widgets for a dashboard tailored to your space.
[Take me to Reports](#) · [Dismiss](#)


Filter

38 completed
in the last 7 days

88 updated
in the last 7 days

88 created
in the last 7 days

0 due soon
in the next 7 days

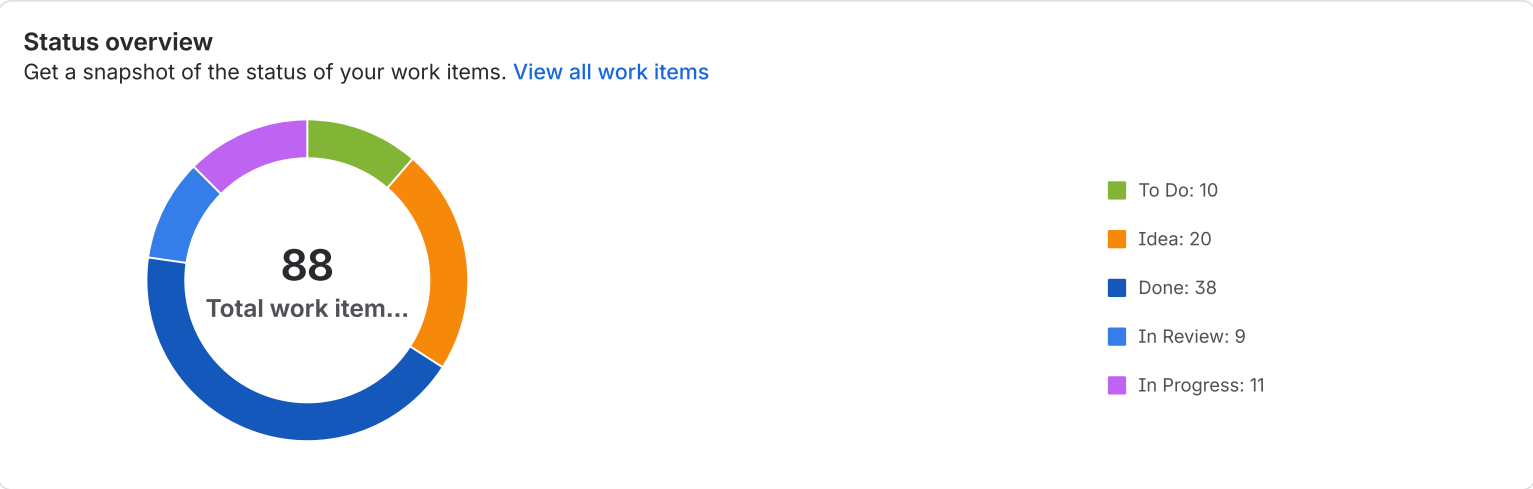

Recent activity
Stay up to date with what's happening across the space.

Today

- sv

SRIMAN VEL updated field "status" on [KAN-39: Online Presence](#) To Do
in less than a minute
- sv


SRIMAN VEL updated field "status" on [KAN-38: Chat Groups](#) To Do
less than a minute ago
- sv

SRIMAN VEL updated field "status" on [KAN-36: AI Provider Failover](#) To Do
less than a minute ago
- sv

SRIMAN VEL updated field "status" on <https://srimankumar06.atlassian.net/browse/KAN-35>


Priority breakdown

Get a holistic view of how work is being prioritized. [How to manage priorities for spaces](#)

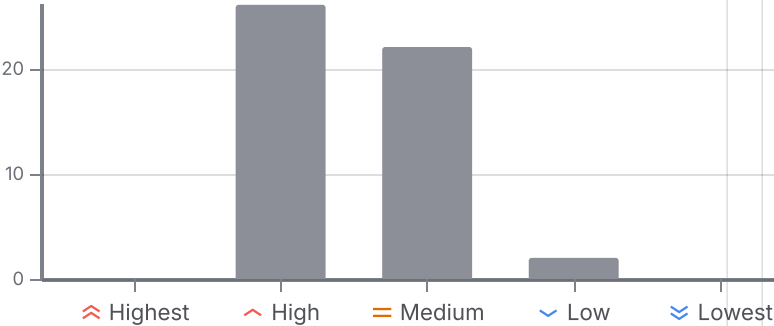


Types of work

Get a breakdown of work items by their types. [View all items](#)

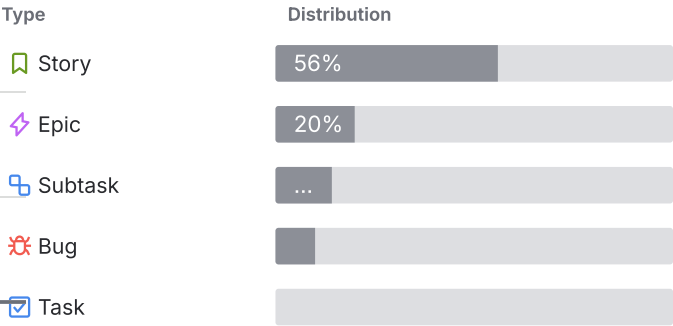


Team workload

Monitor the capacity of your team. [Reassign work items to get the right balance](#)



Epic progress

See how your epics are progressing at a glance. [View all epics](#)

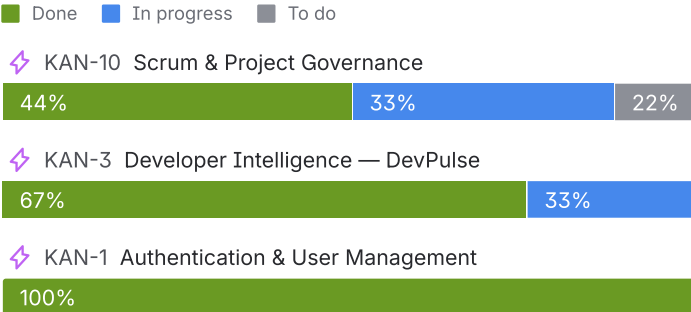

Was the information shown in this page useful? [Give us feedback](#)

- For you

Recent

Starred

Apps

Plans

Spaces

Recent

Alumnex Connect

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Confluence

Assets

Teams

Goals

Projects

Customize sidebar

Spaces

Alumnex Connect

Summary

List

Board

Calendar

Timeline

Docs

Forms

Reports

Goals

Development

More reports

Edit

0 work items

completed in the last ...

88 work items



updated in the last 7 d...




88 work items

created in the last 7 d...

0 work items

due in the next 7 days

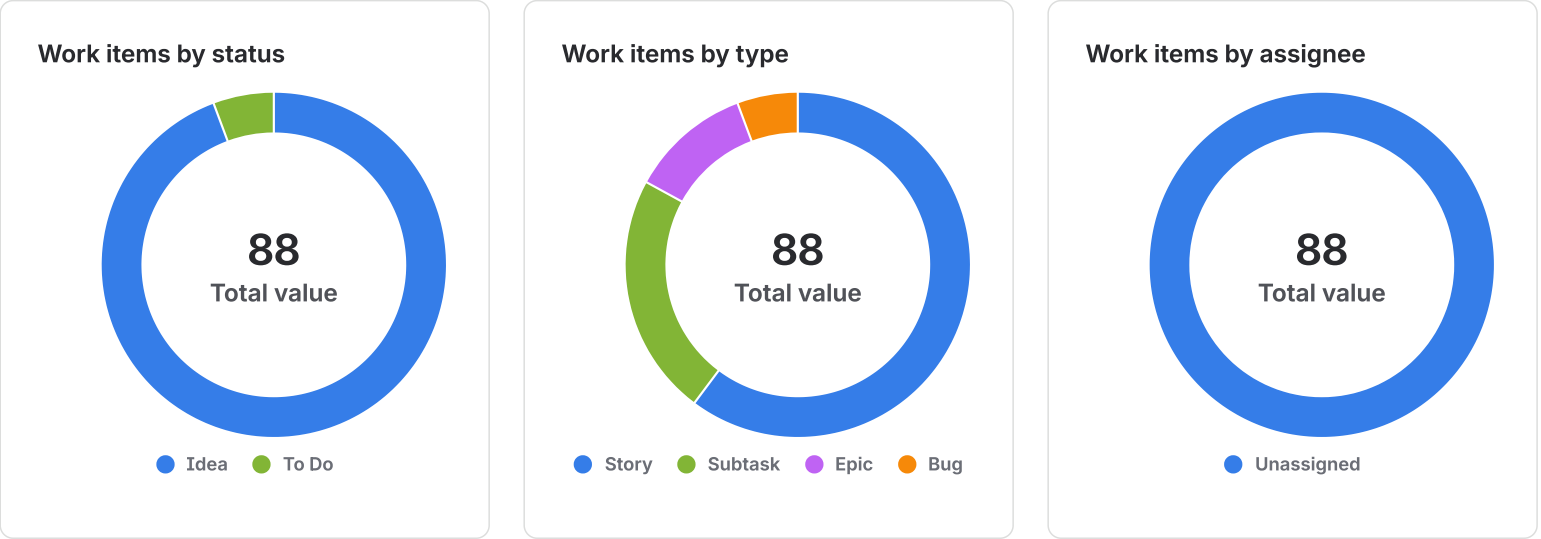

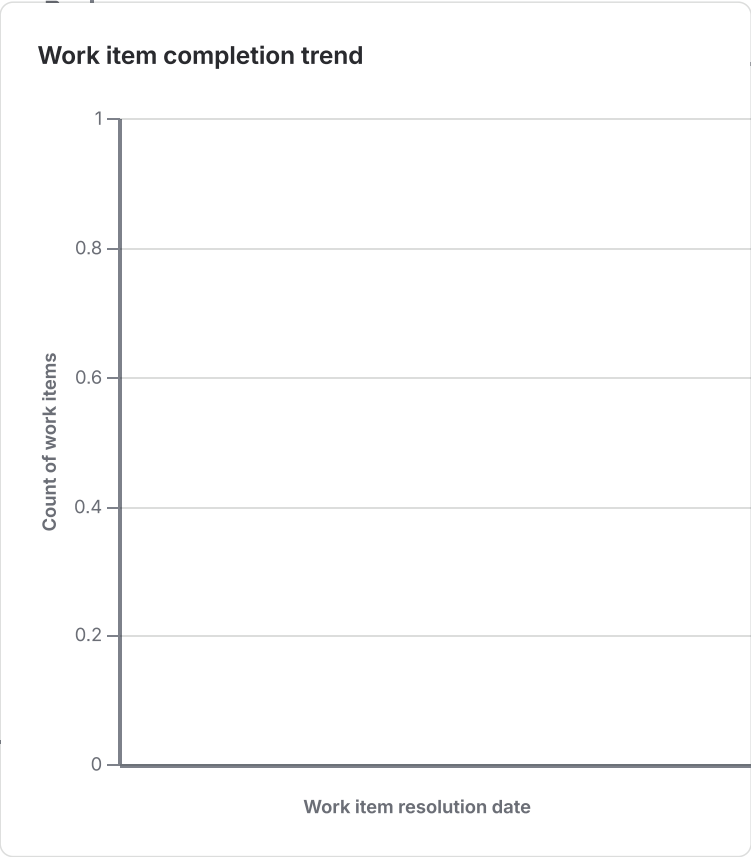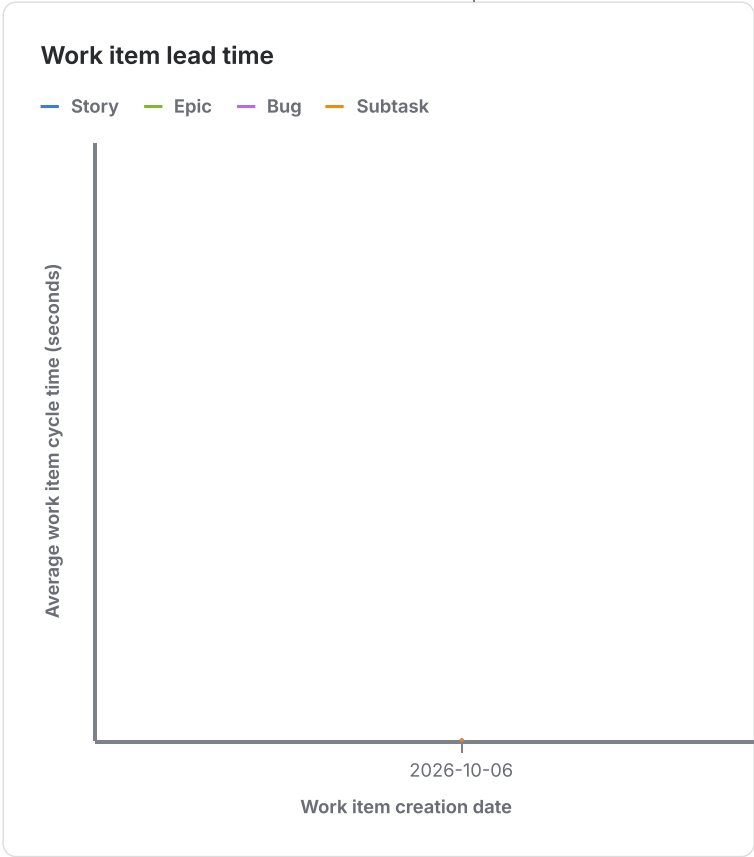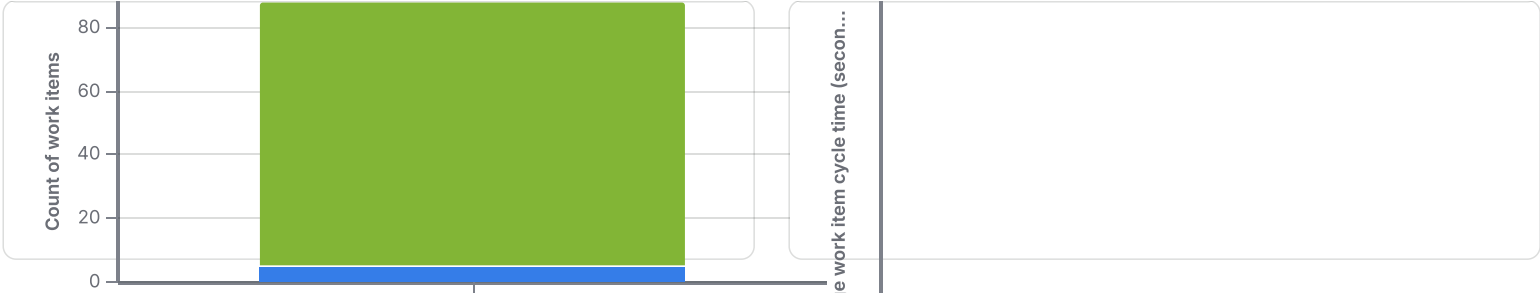

Work item details

Development - Jira			
Work item key ▾	Work type ▾	Work item priority ▾	Issue summary ▾
KAN-1	⚡ Epic	⬆ High	Authentication & User Management
KAN-10	⚡ Epic	⬆ High	Scrum & Project Governance
KAN-11	📖 Story		Student Registration
KAN-12	📖 Story	⬆ Highest	Student Login
KAN-13	📖 Story	⬆ High	OAuth Authentication
KAN-14	📖 Story	⬆ High	OTP / Two-Factor Authentication
KAN-15	📖 Story	⬆ High	User Profile Management
KAN-16	📖 Story	⬆ High	Role-Based Access Control

[https://srinankumar06.atlassian.net/jira/software/projects/KAN/list?ql=project%3D"KAN" AND \(statusCategory 1%3D Done OR \(statusCategory %3D Done AND statusCategoryChangedDate >%3D -2w\)\) ORDER B...](https://srinankumar06.atlassian.net/jira/software/projects/KAN/list?ql=project%3D) 1/1

- For you
- Recent
- Starred
- Apps
- Plans
- Spaces
- Recent
- Alumnex Connect
- More spaces
- Recommended
- Create a roadmap
- Filters
- Dashboards
- Confluence
- Assets
- Teams
- Goals
- Projects
- Customize sidebar

Spaces

Alumnex Connect

SummaryListBoardCalendarTimelineDocsFormsReportsGoalsDevelopment

Ask AISearch w...Filter 2Group

	Work	Assignee	Reporter	Priority
☐	KAN-10 Scrum & Project Governance	Unassigned	SRIMAN VEL	High
☐	KAN-9 Security, Reliability & DevOps	Unassigned	SRIMAN VEL	High
☐	KAN-8 Mobile Application	Unassigned	SRIMAN VEL	High
☐	KAN-7 Community & Events	Unassigned	SRIMAN VEL	High
☐	KAN-6 Real-Time Communication	Unassigned	SRIMAN VEL	High
☐	KAN-5 AI Career Assistant	Unassigned	SRIMAN VEL	High
☐	KAN-4 Career & Job Management	Unassigned	SRIMAN VEL	High
☐	KAN-3 Developer Intelligence — DevPulse	Unassigned	SRIMAN VEL	High
☐	KAN-2 Alumni–Student Mentorship	Unassigned	SRIMAN VEL	High
☐	KAN-1 Authentication & User Management	Unassigned	SRIMAN VEL	High
☐	KAN-68 Google Calendar Scope Access Denied	Unassigned	SRIMAN VEL	Medium
☐	KAN-66 FCM Push Notification Delivery Failure	Unassigned	SRIMAN VEL	High
☐	KAN-65 Duplicate Reminder Notifications	Unassigned	SRIMAN VEL	High
☐	KAN-64 Daily Goal / Streak Synchronization Loss	Unassigned	SRIMAN VEL	High

Double click to collapse

Ctrl [

Create

88 of 88

- 88 of 88 ↺

Template - Project plan

Driver	
Approver	
Contributors	
Informed	
Objective	
Due date	
Key outcomes	
Status	NOT STARTED / IN PROGRESS / COMPLETE

Problem statement

Scope

Must have:	
Nice to have:	
Not in scope:	

Timeline

Milestones and deadlines

Milestone	Owner	Deadline	Status

--	--	--	--

 Related links



Template - Meeting notes



Date



Participants

-
-



Goals



Brainstorm



Discussion topics

Time	Topic	Presenter	Notes
			•



Action items



Decisions



Related info



Template - Weekly status report

 Copy and paste this section for each week.

Win

- 1.
- 2.
- 3.

Needs input

- 1.
- 2.
- 3.

Focus

- 1.
- 2.

Notes	
Important Links	

Alumnex Connect — Jira Project Management & Agile Playbook

Alumnex Connect Jira project-management and Agile/Scrum operating playbook.

Jira is the source of truth for backlog, work status, defects, dependencies, releases and delivery metrics.

Scrum model

- Product Backlog and refinement
- Sprint Planning
- Daily Scrum
- Sprint Review
- Sprint Retrospective
- Definition of Ready / Definition of Done
- Risk, dependency and decision tracking
- Release and version tracking
- Agile metrics and continuous improvement

Product areas

Authentication & User Management; Alumni–Student Mentorship; Developer Intelligence — DevPulse; Career & Job Management; AI Career Assistant; Real-Time Communication; Community & Events; Mobile Application; Security, Reliability & DevOps; Scrum & Project Governance.

Defect lifecycle

Record reproducible defects with observed behavior, expected behavior, impact, acceptance/fix criteria and verification notes. Do not close without validation.

Important configuration note

The current KAN board is a simple/team-managed board and does not support Jira Scrum sprints. Therefore no historical or active sprint records are being fabricated. The Scrum backlog and governance model are represented in Jira now; a Scrum-capable board can later use the same backlog for real Jira Sprints.

Reconstruction note

Because Alumnex Connect is already developed and the Jira project previously contained no issues, the created backlog and governance artifacts are a structured

reconstruction/documentation of project work and operating practices, not claims of historical Sprint execution.

Current observed defects

Daily Goal / Streak Synchronization Loss; Duplicate Reminder Notifications; FCM Push Notification Delivery Failure; Google OAuth Redirect URI Mismatch; Google Calendar Scope Access Denied. Verify each against the current implementation before closure.

Alumnex Connect — Story Point Estimate Baseline

Alumnex Connect — Story Point Estimate Baseline

This page records the **Suggested estimate** values already embedded in the 53 Jira Story descriptions for project KAN. The estimates are a planning baseline, not a claim of historical Sprint execution.

Jira field constraint: the current KAN team-managed project does not expose a Story Points custom field in its issue-type metadata. The estimate values therefore remain documented in each story description and are consolidated here for reporting.

Baseline Summary

Metric	Value
Stories	53
Total suggested story points	256
Highest single estimate	8
Smallest estimate	2

Story-by-Story Register

Jira	Story	Epic	Phase	Points
KAN-11	Student Registration	Authentication & User Management	Phase 1 — Foundation	5
KAN-12	Student Login	Authentication & User Management	Phase 1 — Foundation	5
KAN-13	OAuth Authentication	Authentication & User Management	Phase 1 — Foundation	5

KAN-14	OTP / Two-Factor Authentication	Authentication & User Management	Phase 1 — Foundation	5
KAN-15	User Profile Management	Authentication & User Management	Phase 1 — Foundation	3
KAN-16	Role-Based Access Control	Authentication & User Management	Phase 1 — Foundation	5
KAN-17	Browse Alumni Mentors	Alumni–Student Mentorship	Phase 2 — Mentorship & Career	5
KAN-18	Request Mentorship	Alumni–Student Mentorship	Phase 2 — Mentorship & Career	5
KAN-19	Manage Mentorship Requests	Alumni–Student Mentorship	Phase 2 — Mentorship & Career	5
KAN-20	Mentorship Session Tracking	Alumni–Student Mentorship	Phase 2 — Mentorship & Career	5
KAN-21	Mentorship Reviews	Alumni–Student Mentorship	Phase 2 — Mentorship & Career	3
KAN-22	GitHub Developer Statistics	Developer Intelligence — DevPulse	Phase 3 — DevPulse	5
KAN-23	LeetCode Statistics	Developer Intelligence — DevPulse	Phase 3 — DevPulse	5
KAN-24	Codeforces Statistics	Developer Intelligence —	Phase 3 — DevPulse	5

		DevPulse		
KAN-25	Unified Developer Profile	Developer Intelligence — DevPulse	Phase 3 — DevPulse	3
KAN-26	Activity Hub	Developer Intelligence — DevPulse	Phase 3 — DevPulse	8
KAN-27	Streak Tracking	Developer Intelligence — DevPulse	Phase 3 — DevPulse	5
KAN-28	Job Posting	Career & Job Management	Phase 2 — Mentorship & Career	5
KAN-29	Browse Job Opportunities	Career & Job Management	Phase 2 — Mentorship & Career	5
KAN-30	Apply for Jobs	Career & Job Management	Phase 2 — Mentorship & Career	5
KAN-31	Job Application Management	Career & Job Management	Phase 2 — Mentorship & Career	5
KAN-32	ATS Resume Analysis	Career & Job Management	Phase 2 — Mentorship & Career	8
KAN-33	AI Career Mentor	AI Career Assistant	Phase 4 — AI & Communication	8
KAN-34	Skill Gap Analysis	AI Career Assistant	Phase 4 — AI & Communication	8
KAN-35	AI Mock Interview	AI Career Assistant	Phase 4 — AI & Communication	8

KAN-36	AI Provider Failover	AI Career Assistant	Phase 4 — AI & Communication	5
KAN-37	Real-Time Chat	Real-Time Communication	Phase 4 — AI & Communication	8
KAN-38	Chat Groups	Real-Time Communication	Phase 4 — AI & Communication	5
KAN-39	Online Presence	Real-Time Communication	Phase 4 — AI & Communication	3
KAN-40	Read Receipts	Real-Time Communication	Phase 4 — AI & Communication	3
KAN-41	Real-Time Notifications	Real-Time Communication	Phase 4 — AI & Communication	5
KAN-42	Community Forum	Community & Events	Phase 4 — AI & Communication	5
KAN-43	Event Management	Community & Events	Phase 4 — AI & Communication	5
KAN-44	Alumni Networking	Community & Events	Phase 4 — AI & Communication	5
KAN-45	Android Mobile Wrapper	Mobile Application	Phase 5 — Mobile & Reliability	8
KAN-46	Mobile Authentication	Mobile Application	Phase 5 — Mobile & Reliability	5
KAN-47	Mobile Responsive UI	Mobile Application	Phase 5 — Mobile & Reliability	5
KAN-48	Mobile Notifications	Mobile Application	Phase 5 — Mobile & Reliability	5

KAN-49	Android APK Build & Release	Mobile Application	Phase 5 — Mobile & Reliability	3
KAN-50	Security Hardening	Security, Reliability & DevOps	Phase 5 — Mobile & Reliability	8
KAN-51	API Failover	Security, Reliability & DevOps	Phase 5 — Mobile & Reliability	5
KAN-52	Automated Testing	Security, Reliability & DevOps	Phase 5 — Mobile & Reliability	5
KAN-53	CI/CD Pipeline	Security, Reliability & DevOps	Phase 5 — Mobile & Reliability	5
KAN-54	Production Monitoring	Security, Reliability & DevOps	Phase 5 — Mobile & Reliability	3
KAN-55	Product Backlog & Refinement	Scrum & Project Governance	Phase 1 — Foundation	3
KAN-56	Sprint Planning	Scrum & Project Governance	Phase 1 — Foundation	3
KAN-57	Daily Scrum Tracking	Scrum & Project Governance	Phase 1 — Foundation	2
KAN-58	Sprint Review & Stakeholder Feedback	Scrum & Project Governance	Phase 1 — Foundation	3
KAN-59	Sprint Retrospective & Improvement Actions	Scrum & Project Governance	Phase 1 — Foundation	3

KAN-60	Definition of Ready & Definition of Done	Scrum & Project Governance	Phase 1 — Foundation	3
KAN-61	Risk, Dependency & Decision Tracking	Scrum & Project Governance	Phase 1 — Foundation	3
KAN-62	Release & Version Tracking	Scrum & Project Governance	Phase 1 — Foundation	3
KAN-63	Agile Metrics & Continuous Improvement	Scrum & Project Governance	Phase 1 — Foundation	3

Operational Use

- Use the points as the planning baseline when splitting work into future iterations.
- Do not interpret the values as completed velocity because the current KAN board is team-managed/simple and has no Jira Scrum Sprint history.
- When the project is migrated to a configuration exposing a Story Points field, these values can be transferred into that field without changing the backlog intent.

Source of estimates: the existing KAN story descriptions, each containing a “Suggested estimate” value.

Practical Scrum Process Using Jira

Running Example

Project Name

Student Management System (SMS)

Customer

ABC Engineering College

Requirement

ABC Engineering College wants a web application where students can:

- Register
- Login
- Search available courses
- Enroll in courses
- View examination results
- Update profile

The college gives **3 months** to complete the project.

Step 1: Customer Gives Requirements

The Scrum process starts when the customer meets the software company.

Customer says:

"Our college currently maintains student information manually. We need a web-based Student Management System. Students should be able to register, log in, search courses, enroll in courses, and view their semester results. The system should also allow administrators to manage student records."

The Business Analyst (or Product Owner) collects these requirements.

Raw Requirements

Requirement ID	Requirement
R1	Student Registration
R2	Student Login
R3	Search Courses
R4	Course Enrollment
R5	View Results
R6	Update Student Profile

At this stage, these are just business requirements—they are **not yet entered into Jira**.

Step 2: Scrum Team Formation

The company forms a Scrum Team.

Role	Person	Responsibility
Product Owner	Priya	Understands customer requirements and manages the Product Backlog
Scrum Master	Rahul	Facilitates Scrum meetings and removes obstacles
Front-end Developer	Arun	Develops the user interface
Back-end Developer	Meena	Develops APIs and business logic
Database Developer	Kumar	Designs and manages the database
Tester	Kavitha	Tests the application

The Product Owner is responsible for creating work items in Jira.

Step 3: Login to Jira

Open the Jira URL provided by the organization.

Example:

<https://companyname.atlassian.net>

After logging in, the Jira Dashboard appears.

The dashboard may contain:

- Projects
- Assigned Issues
- Recent Activity
- Sprint Progress
- Reports

Step 4: Create a Scrum Project in Jira

The Product Owner creates a new project.

Navigation

Projects



Create Project



Software Development



Scrum

Fill the Project Details

Field	Value
Project Name	Student Management System
Project Key	SMS
Project Lead	Priya
Template	Scrum

Click **Create**.

Jira creates the project.

What Jira Creates Automatically

Once the project is created, Jira automatically provides several components.

Jira Component	Purpose
Backlog	Stores all future work items
Active Sprint Board	Displays work currently being developed
Issues	Stores Stories, Tasks, Bugs, and Epics
Reports	Burndown Chart, Velocity Chart, Sprint Report
Releases	Tracks software versions

At this point, the project exists, but it contains **no work items yet**.

Step 5: Understanding the Product Backlog

Before creating issues in Jira, students should understand **what a Product Backlog is**.

A **Product Backlog** is an ordered list of everything that may be needed in the product.

Think of it as a **master to-do list** maintained by the Product Owner.

Initially, our backlog is empty.

Student Management System

Backlog

No Issues Found

Now the Product Owner starts converting the customer's requirements into **User Stories**.

Step 6: What is a User Story?

A **User Story** describes a feature from the perspective of an end user.

The standard format is:

As a <user>

I want to <perform an action>

So that <I receive a benefit>

Example 1

Requirement:

Student Registration

User Story:

As a student, I want to register so that I can create my account and access the Student Management System.

Example 2

Requirement:

Student Login

User Story:

As a student, I want to log in using my username and password so that I can securely access my account.

Example 3

Requirement:

Search Courses

User Story:

As a student, I want to search available courses so that I can enroll in subjects of my choice.

Example 4

Requirement:

View Results

User Story:

As a student, I want to view my semester results so that I can check my academic performance.

Step 7: Creating the First User Story in Jira

Now the Product Owner enters the first story into Jira.

Navigation

Backlog



Create Issue

The "Create Issue" form opens.

Fill it as follows.

Field	Sample Value
Project	Student Management System
Issue Type	Story
Summary	Student Registration

Field	Sample Value
Description	As a student, I want to register so that I can create my account and access the Student Management System.
Priority	High
Story Points	5
Assignee	Unassigned (or leave blank initially)
Reporter	Priya
Labels	registration

Click **Create**.

The first story is now added to the Product Backlog.

Product Backlog After Creating the First Story

The backlog now looks like this.

Issue Key	Issue Type	Summary	Priority	Story Points	Status
SMS-1	Story	Student Registration	High	5	To Do

Why 5 Story Points?

The team estimates that Registration requires:


- Designing the registration page
- Creating the student table
- Input validation
- Password encryption
- Email validation
- Database integration
- Testing

Since it involves several activities, the team estimates **5 Story Points**.

Current Project Status

At this stage, the Jira project contains:

Project



No sprint has been created yet. No developer has been assigned. No work has started.

Creating the Product Backlog, Epics, User Stories and Sprint 1

Previous Status

- ✓ Project Created
- ✓ Scrum Team Formed
- ✓ First User Story Created

Now the Product Owner continues building the complete Product Backlog.

Step 8: Why Do We Need Epics?

Suppose the customer gives the following requirements.

Requirement	Description
Student Registration	Students should register
Student Login	Students should login
Forgot Password	Password recovery

Requirement	Description
Update Profile	Edit profile
Search Courses	Search available courses
Course Enrollment	Register for a course
View Results	Check semester results
Download Marksheet	Download marksheet

The Product Owner thinks:

"There are many related stories. Instead of keeping them separately, I can group them."

In Jira, **Epics** are used for grouping related user stories.

Think of an Epic as a **large feature**.

Example

Feature

↓

Student Account Management
contains

- Registration
- Login
- Forgot Password
- Update Profile

Step 9: Creating Epics in Jira

Navigation

Backlog

↓

Epics Panel

↓

Create Epic

Epic 1

Field	Value
Issue Type	Epic
Epic Name	Student Account Management
Summary	Student Account Management
Description	Features related to student account creation and maintenance

Click

Create

Epic 2

Course Management

Description

Students can search and enroll in courses.

Epic 3

Examination Management

Description

Students can view results and download marksheets.

Now the backlog displays

EPICS

Student Account Management

Course Management

Examination Management

Step 10: Creating User Stories

The Product Owner now creates all stories.

Story 1

Navigation

Create Issue

Fill

Field	Value
Issue Type	Story
Summary	Student Registration
Description	As a student, I want to register so that I can access the Student Management System.
Epic	Student Account Management
Priority	High
Story Points	5

Click

Create

Story 2

Field	Value
Summary	Student Login
Description	As a student, I want to login using username and password so that I can securely access my account.
Epic	Student Account Management
Story Points	3

Story 3

Field	Value
Summary	Forgot Password
Description	As a student, I want to reset my password so that I can regain access if I forget it.
Epic	Student Account Management
Story Points	5

Story 4

Field	Value
Summary	Update Profile
Description	As a student, I want to update my profile information so that my details remain current.
Epic	Student Account Management
Story Points	5

Story 5

Field	Value
Summary	Search Courses
Description	As a student, I want to search available courses so that I can choose subjects.
Epic	Course Management
Story Points	8

Story 6

Field	Value
Summary	Course Enrollment
Description	As a student, I want to enroll in selected courses so that I can attend classes.
Epic	Course Management
Story Points	8

Story 7

Field	Value
Summary	View Results
Description	As a student, I want to view semester results so that I can know my performance.
Epic	Examination Management
Story Points	5

Story 8

Field	Value
Summary	Download Marksheet
Description	As a student, I want to download my marksheet so that I can print it whenever needed.
Epic	Examination Management
Story Points	3

Product Backlog

Now Jira shows

Key	Story	Epic	Priority	Story Points
SMS-1	Student Registration	Student Account Management	High	5
SMS-2	Student Login	Student Account Management	High	3
SMS-3	Forgot Password	Student Account Management	Medium	5
SMS-4	Update Profile	Student Account Management	Low	5
SMS-5	Search Courses	Course Management	Medium	8
SMS-6	Course Enrollment	Course Management	High	8
SMS-7	View Results	Examination Management	Medium	5
SMS-8	Download Marksheet	Examination Management	Low	3

Step 11: Prioritize the Product Backlog

The Product Owner arranges the stories according to business importance.

The customer says:

"Without Registration and Login, nothing else can work."

Therefore, those stories are moved to the top.

Highest Priority

Registration

↓

Login

↓

Course Enrollment

↓

Search Courses

↓

View Results

↓

Forgot Password

↓

Update Profile

↓

Download Marksheet

Step 12: Story Point Estimation Meeting

Before starting development, the Scrum Team estimates the effort required for each story.

Story	Discussion	Story Points
Registration	UI + API + Database + Validation + Testing	5
Login	UI + Authentication + Testing	3
Forgot Password	OTP + Email + Database + Testing	5
Search Courses	Search + Filters + Database Queries	8
Enrollment	Validation + Database + Business Rules	8
Results	Retrieve Results + Display	5
Marksheet	Generate PDF + Download	3

Example

Product Owner: "How much effort will Registration take?"

Frontend Developer: "I need two days for the registration page."

Backend Developer: "I need two days for the API."

Tester: "I need one day for testing."

The team agrees on **5 Story Points**.

Note: Story Points estimate **effort and complexity**, not the number of hours.

Step 13: Create Sprint 1

The Product Owner decides to start the first sprint.

Navigation

Backlog



Create Sprint

Jira creates

Sprint 1

Step 14: Move Stories into Sprint 1

The team estimates that they can complete about **16 Story Points** in two weeks.

The Product Owner drags the following stories into Sprint 1:

Story	Story Points
Student Registration	5
Student Login	3
Forgot Password	5
Download Marksheet	3
Total	16

Why not include Course Enrollment (8 points)?

Adding it would exceed the team's capacity ($16 + 8 = 24$ points), making the sprint unrealistic.

Sprint 1 Backlog

Sprint 1

Registration

Login

Forgot Password

Download Marksheet

The remaining stories stay in the Product Backlog for future sprints.

Step 15: Start Sprint 1

Click

Start Sprint

Fill the details.

Field	Value
Sprint Name	Sprint 1
Duration	2 Weeks
Start Date	1 July
End Date	14 July

Field	Value
Sprint Goal	Students should be able to register, log in, recover passwords, and download marksheets.
Click Start	

Active Sprint Board

The Scrum Board initially appears as:

TO DO

SMS-1 Registration

SMS-2 Login

SMS-3 Forgot Password

SMS-8 Download Marksheet

IN PROGRESS

None

DONE

None

Working Inside Sprint 1 (Tasks, Subtasks, Board, Daily Scrum, Bugs)

Current Status

Sprint 1 contains:

Issue Key	Story	Story Points
SMS-1	Student Registration	5
SMS-2	Student Login	3
SMS-3	Forgot Password	5
SMS-8	Download Marksheet	3

Sprint Capacity = **16 Story Points**

Now the development team starts working.

Step 16: Sprint Planning Meeting

The Sprint Planning Meeting is held on the first day of the sprint.

Participants

- Product Owner
- Scrum Master
- Developers
- Tester

Objective

The Product Owner explains each selected user story.

Example:

Story SMS-1

Student Registration

As a student, I want to register so that I can create my account and access the Student Management System.

The team discusses:

- What needs to be developed?
- How long will it take?
- Who will perform the work?

The team decides to divide this story into smaller tasks.

Step 17: Breaking a Story into Tasks

In Jira, open:

SMS-1 Student Registration

Click

Create Child Issue

or (depending on the Jira configuration)

More



Create Sub-task

Story

SMS-1


Student Registration

Tasks Created

Task ID	Task Name	Assigned To
SMS-9	Design Registration Page	Arun
SMS-10	Create Student Database Table	Kumar
SMS-11	Develop Registration API	Meena
SMS-12	Validate Registration Form	Arun
SMS-13	Test Registration Module	Kavitha

Jira hierarchy:

SMS-1 Student Registration



Step 18: Creating Subtasks

Now consider the task:

SMS-11

Develop Registration API

This task is still large.

The backend developer breaks it into subtasks.

Subtasks


Subtask	Description
Create REST API	Build POST /register API
Validate Email	Ensure email format is valid
Encrypt Password	Store passwords securely
Save Student Data	Insert into the database
Return Success Response	Send registration success message

Hierarchy:

Story

SMS-1 Registration



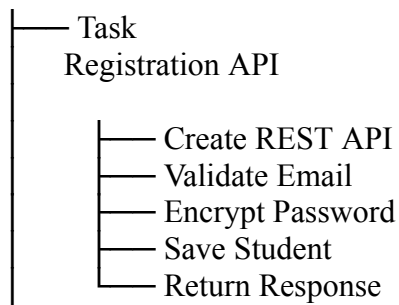

Step 19: Assigning Work

Each issue is assigned to a team member.

In Jira, open an issue.

Example:

SMS-11 Registration API

Edit the **Assignee** field.

Choose:

Meena

Repeat for all tasks.

Task	Assignee
Registration UI	Arun
Student Table	Kumar
Registration API	Meena
Input Validation	Arun
Testing	Kavitha

Now every team member knows what to work on.

Step 20: Active Sprint Board

Open:

Board

Initially, all work is in **To Do**.

TO DO

SMS-1 Registration

SMS-2 Login

SMS-3 Forgot Password

SMS-8 Download Marksheet

IN PROGRESS

None

DONE

None

Step 21: Developers Start Working

Day 1

Arun starts designing the registration page.

He opens:

SMS-9

Design Registration Page

Changes the status:

To Do



In Progress

The Scrum Board becomes:

TO DO

Login

Forgot Password

Download Marksheet

IN PROGRESS

Registration UI

DONE

None

Day 2

Arun completes the UI.

Status changes:

Done

Board:

TO DO

Login

Forgot Password

Download Marksheet

Registration API

IN PROGRESS

None

DONE

Registration UI

Now Meena starts developing the Registration API.

Step 22: Daily Scrum Meeting

Every morning at 9:30 AM, the Scrum Team gathers for a **15-minute Daily Scrum**.

Each member answers **three questions**.

Developer Arun

Yesterday

Completed the Registration UI.

Today

Will support form validation.

Blockers

None.

Developer Meena**Yesterday**

Started Registration API.

Today

Complete API and integrate with the database.

Blockers

Waiting for the student database table.

Database Developer Kumar**Yesterday**

Created the Student table.

Today

Create indexes and constraints.

Blockers

None.

Tester Kavitha**Yesterday**

Prepared Registration test cases.

Today

Test completed Registration functionality.

Blockers

Waiting for API completion.

Scrum Master

The Scrum Master notices that Meena is blocked because the database table is not fully ready. He coordinates with Kumar to complete the database work quickly so Meena can continue without delay.

Important: The Daily Scrum is **not** for solving problems. It is used to identify blockers. Detailed discussions happen after the meeting.

Step 23: Updating the Scrum Board

As work progresses, team members update issue status.

Example:

Registration API

To Do

↓

In Progress

↓

Code Review

↓

Done

Depending on the Jira workflow, additional statuses such as **Code Review** or **Testing** may exist.

Step 24: Testing

Once development is complete, the Tester begins testing.

Example:

SMS-13

Test Registration Module

Test Cases

Test Case	Expected Result
Valid Registration	Registration Successful
Duplicate Email	Display "Email already exists"
Blank Name	Show validation message
Invalid Email	Show invalid email error
Weak Password	Ask user to choose a stronger password

Step 25: Bug Found

During testing, Kavitha discovers a defect.

Problem:

Duplicate email registration is allowed.

She creates a Bug in Jira.

Navigation

Create Issue

Select:

Issue Type

Bug

Bug Details

Field	Value
Issue Type	Bug
Summary	Duplicate email registration allowed
Description	The system allows two students to register with the same email address.
Priority	High
Assignee	Meena
Reporter	Kavitha
Linked Issue	SMS-1 Student Registration

Click **Create**.

Jira generates:

SMS-14

Duplicate Email Registration Allowed

Step 26: Bug Lifecycle

The bug progresses through the workflow:

Open

↓

Assigned
↓
In Progress
↓
Fixed
↓
Retesting
↓
Closed

After Meena fixes the bug, Kavitha retests it.
If the issue is resolved, she changes the status to **Closed**.

Step 27: Completing a Story

When all tasks and bugs related to **SMS-1 Student Registration** are complete:

- All tasks are marked **Done**.
- All subtasks are complete.
- All linked bugs are closed.

The Product Owner reviews the feature and accepts it.

The story status changes to:

Done

Scrum Board After One Week

TO DO

Forgot Password

Download Marksheet

IN PROGRESS

Login

DONE

Registration

The board clearly shows the team's progress.

What Students Learn from Part 3

By the end of this part, students understand:

- How a **Story** is divided into **Tasks**.
- How **Tasks** can be divided into **Subtasks**.
- How work is assigned to team members.
- How the **Scrum Board** reflects progress.
- The purpose and structure of the **Daily Scrum**.
- How **Bugs** are created, assigned, fixed, and closed in Jira.
- How a story is completed and accepted.

Sprint Review, Sprint Retrospective, Jira Reports, Closing Sprint & Starting Sprint 2

Current Status

At the end of Part 3

Sprint 1 contains:

Story ID	Story	Status
SMS-1	Student Registration	✓ Done
SMS-2	Student Login	✓ Done
SMS-3	Forgot Password	✓ Done
SMS-8	Download Marksheet	✓ Done

The Sprint Board now shows
TO DO

None

IN PROGRESS

None

DONE

SMS-1 Registration

SMS-2 Login

SMS-3 Forgot Password

SMS-8 Download Marksheet

The sprint duration (2 weeks) has ended.
Now Scrum enters the next phase.

Step 28: Sprint Review Meeting

Purpose

To demonstrate the completed software to the customer and collect feedback.

Participants

- Product Owner
- Scrum Master
- Developers
- Tester
- Customer

Product Owner Demonstrates the Software

Feature 1

Student Registration

Developer demonstrates

Register Student

Name

Email

Password

Confirm Password

[Register]

Customer registers a student.

Output

Registration Successful

Customer is satisfied.

Feature 2

Student Login

Customer enters

Username

Password

[Login]

Output

Welcome

Saravanan

Customer is satisfied.

Feature 3

Forgot Password

Customer clicks

Forgot Password

System sends OTP.

Customer comments

OTP expiry should be 5 minutes instead of 10 minutes.

This requirement was never discussed before.

Feature 4

Download Marksheet

Customer downloads the PDF.

Customer says

Please add the College Logo in the marksheet.

Again, this is a **new requirement**.

Step 29: Creating New Stories from Customer Feedback

The Product Owner immediately opens Jira.

Navigation

Backlog

↓

Create Issue

Story 1

Field	Value
Issue Type	Story
Summary	Reduce OTP expiry to 5 minutes
Epic	Student Account Management

Field	Value
Priority	Medium
Story Points	2

Story 2

Field	Value
Issue Type	Story
Summary	Add College Logo to Marksheet
Epic	Examination Management
Priority	Low
Story Points	3

These stories are **not added to Sprint 1** because the sprint has already ended.
They are placed in the **Product Backlog**.

Updated Product Backlog

Key	Story	Status
SMS-5	Search Courses	Backlog
SMS-6	Course Enrollment	Backlog
SMS-7	View Results	Backlog
SMS-15	Reduce OTP Expiry	Backlog
SMS-16	Add College Logo	Backlog

Important Scrum Rule

Many beginners ask

Why not simply modify Sprint 1?

Because

A Sprint is considered complete when its time box ends.

Any new requirement goes into the **Product Backlog** and is planned for a future sprint.

Step 30: Sprint Retrospective

Now the customer leaves.

Only the Scrum Team remains.

Participants

- Scrum Master
- Product Owner
- Developers
- Tester

The Scrum Master asks

What went well?

Developer Arun

Registration UI was completed ahead of schedule.

Developer Meena

API integration was smooth.

Tester Kavitha

Only one major bug was found.

What did not go well?

Database Developer Kumar

Database design started late.

Tester

Testing began only after all coding was finished.

Improvements for Next Sprint

The team decides

- Prepare the database before development begins.
- Developers should write unit tests earlier.
- Conduct code reviews daily.
- Test continuously instead of waiting until the end.

The Scrum Master records these action items.

Step 31: Close Sprint 1

Navigation

Board

↓

Complete Sprint

Jira asks

Are you sure you want to complete Sprint 1?

Click

Complete Sprint

Sprint 1 is now closed.

Step 32: Sprint Report

Navigation

Reports

↓

Sprint Report

Jira displays

Story	Status
Registration	Completed
Login	Completed
Forgot Password	Completed
Download Marksheet	Completed

The report also shows

Completed Stories

4

Incomplete Stories

0

Total Story Points

16

Completed Story Points

16

Step 33: Burndown Chart

Navigation

Reports




Burndown Chart

Jira automatically generates the Burndown Chart.

Example

Story Points Remaining

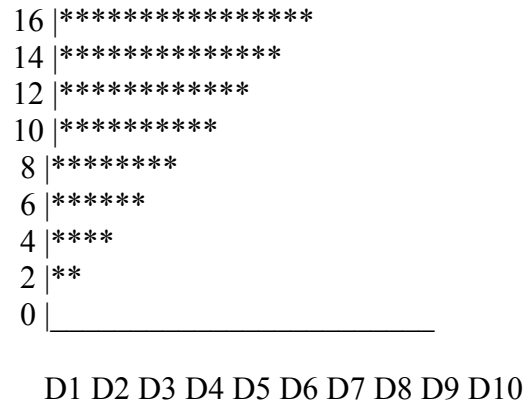

Interpretation

Day 1

16 points remaining

Day 5

8 points remaining

Day 10

0 points remaining

Meaning

The team completed all planned work before the sprint ended.

Step 34: Velocity Chart

Navigation

Reports



Velocity Chart

Since only one sprint has been completed

Sprint 1

Committed

16 Story Points

Completed

16 Story Points

After several sprints, the chart might look like:

Sprint	Committed	Completed
Sprint 1	16	16
Sprint 2	18	17
Sprint 3	20	19
Sprint 4	18	18

Why is the Velocity Chart important?

If the team consistently completes around **18 Story Points**, then in future Sprint Planning, the Product Owner should assign approximately **18 Story Points**, avoiding unrealistic workloads.

Step 35: Create Sprint 2

Navigation

Backlog



Create Sprint

Jira creates

Sprint 2

Step 36: Move Stories into Sprint 2

Remaining backlog

Story	Story Points
Search Courses	8
Course Enrollment	8
View Results	5
OTP Expiry	2
College Logo	3

Team Capacity

18 Story Points

The Product Owner selects

Story	Story Points
Search Courses	8
Course Enrollment	8
OTP Expiry	2
Total	18

These stories are moved into Sprint 2.

Step 37: Start Sprint 2

Sprint Details

Field	Value
Sprint Name	Sprint 2
Duration	2 Weeks
Goal	Students should search and enroll in courses, and the OTP expiry should be reduced to 5 minutes.

Click

Start Sprint
Sprint 2 begins.

Complete Jira Scrum Workflow

